



Korean Culture Festival

Dublin

Student Anna Kovalenko
(TL_KCOMP_B_Y4)

Table of Contents

1. Background to Project.....	3
1.1. Justification.....	3
1.2. Sponsor.....	3
1.3. Objectives.....	3
1.4. Project Life Cycle.....	3
2. Scope Statement.....	4
2.1. Project Scope.....	4
2.2. Project Exclusions.....	4
2.3. Success Criteria.....	5
3. Work Breakdown Structure (WBS).....	6
3.1. Work Breakdown Structure Overview.....	7
4. Organization Chart.....	10
4.1. Organization Chart Overview.....	11
4.2. Organization Structure.....	12
5. Gantt Chart.....	13
6. Budget.....	13
6.1. Project Cost Estimate.....	15
6.2. Contract Types.....	17
6.3. Contract Types Justifications.....	18
7. Communications Plan.....	22
7.1. Communication Objectives.....	22
7.2. Stakeholders and Responsibilities.....	22
7.3. Communication Methods.....	23
7.4. Meetings.....	23
7.5. Reports.....	24
8. Risk Analysis.....	26

9. Project Chapter.....	29
10. Event Day Schedule.....	35
Appendix.....	37
Appendix 2.....	42
Appendix 3.....	45

1. Background to Project

1.1. Justification

My project is to create a Korean Culture Festival based on the growth of interest in Korean Pop (K-pop) and Korean dance and other areas of Korean culture in Ireland. There has been a significant increase in the interest in Korean culture, music and dance as well as traditional art forms, food and cultural practices. However, despite this demand for a Korean Culture Festival, there does not exist at present a recognized festival or professionally run competition to promote K-pop dance and other Korean cultural events in Dublin. The goal of this project is to fill that void with the establishment of an annual event which will promote and celebrate Korea's diverse cultures exchanges between Ireland and Korea. It will provide a platform for both Irish and International performers to showcase their talents and deliver an entertaining and culturally experience to attendees.

1.2. Sponsor

The Korean Embassy in Dublin is the primary sponsor of the project. The festival directly supports the Embassy's goals of promoting Korean culture, fostering community engagement, and strengthening Ireland-Korea relations through soft-power cultural initiatives.

1.3. Objectives

1. A successful hosting event that promotes the Korean Culture and its music in a formal atmosphere.
2. Securing a minimum of 30 entries for the competition and achieving 80% of ticket sale capacity.
3. High technical quality of production in respect to technical issues and equalness of the judging officers.

1.4. Project Life Cycle

The Korean Culture Festival uses the Predictive life cycle due to having a defined scope, a set date for the event, a fixed list of what will be delivered, and distinct phases that include planning, marketing, logistics, setting up the competition,

running the event, and reviewing after the event. A predictive project can plan the timing, cost, and resource needs of the project with a high degree of confidence since the key requirements of the project (location, entertainers, judges, ticketing, safety policies, schedule, etc.) are known and don't often change.

A project using an Adaptive (ASD) life cycle is used for technology or software development when the requirements of the project are changing, the components of the product are being built in an iterative fashion, and the team is learning as it develops the product. Due to the lack of iterative design and changing requirements for this festival, the use of an adaptive process would increase both the complexity and the risk of the project, which are not suit for the project.

2.Scope Statement

2.1. Project Scope

The scope of this project includes planning, coordination, execution, and post-event management of the first-ever annual Korean Culture Festival and includes all logistical and venue responsibilities. The project also includes development of rules and categories for the competitions, management of the on-line registration portal, engagement and coordination of judges, organization of cultural programs to be performed, demonstrated and/or offered at the festival. In addition, marketing and sales functions are part of the project scope, as well as volunteer recruitment, training and management and management of event day personnel. All aspects of vendor procurement, contract administration, resources allocation, budgeting and financial reporting are included, as well as coordination with the Korean Embassy in Dublin as the project's sponsor.

Key areas that are within the scope of this project include:

- Venue management, logistics, and technical setup
- Planning of competitions, coordination of judges, and award of prizes
- Public marketing, ticket sales, and communication
- Recruitment, training and management of volunteers and vendors
- Financial oversight, reporting and coordination with the Korean Embassy in Dublin

All other events and or travel arrangements beyond the first annual event are excluded from the scope of this project.


2.2. Project Exclusions

1. All Festival Management Activities that occur prior to, during and after the festival date.
2. All activities related to the booking/management of local K-pop cover bands for all non-registered competitor and/or contracted performer/workshop host general performances at the festival.
3. The full scope of managing outside vendors in food and/or merchandise kiosks. However, only includes providing a specific area for the vendor and does NOT include procuring/sourcing, hiring and supervising those vendors.
4. Provisioning or sales of merchandise to be sold after the festival date.

2.3. Success Criteria

1. The competition and festival program will be completed in accordance with the established time schedule and without significant delays.
2. Participant and audience surveys after the event have a 4.0 average rating or above on a scale of 1-5.
3. Legal, health, and safety regulations are all fulfilled, with no serious incident(s) occurring.
4. This project has been implemented within a 10% variance of the final approved budget.

3. Work Breakdown Structure (WBS)

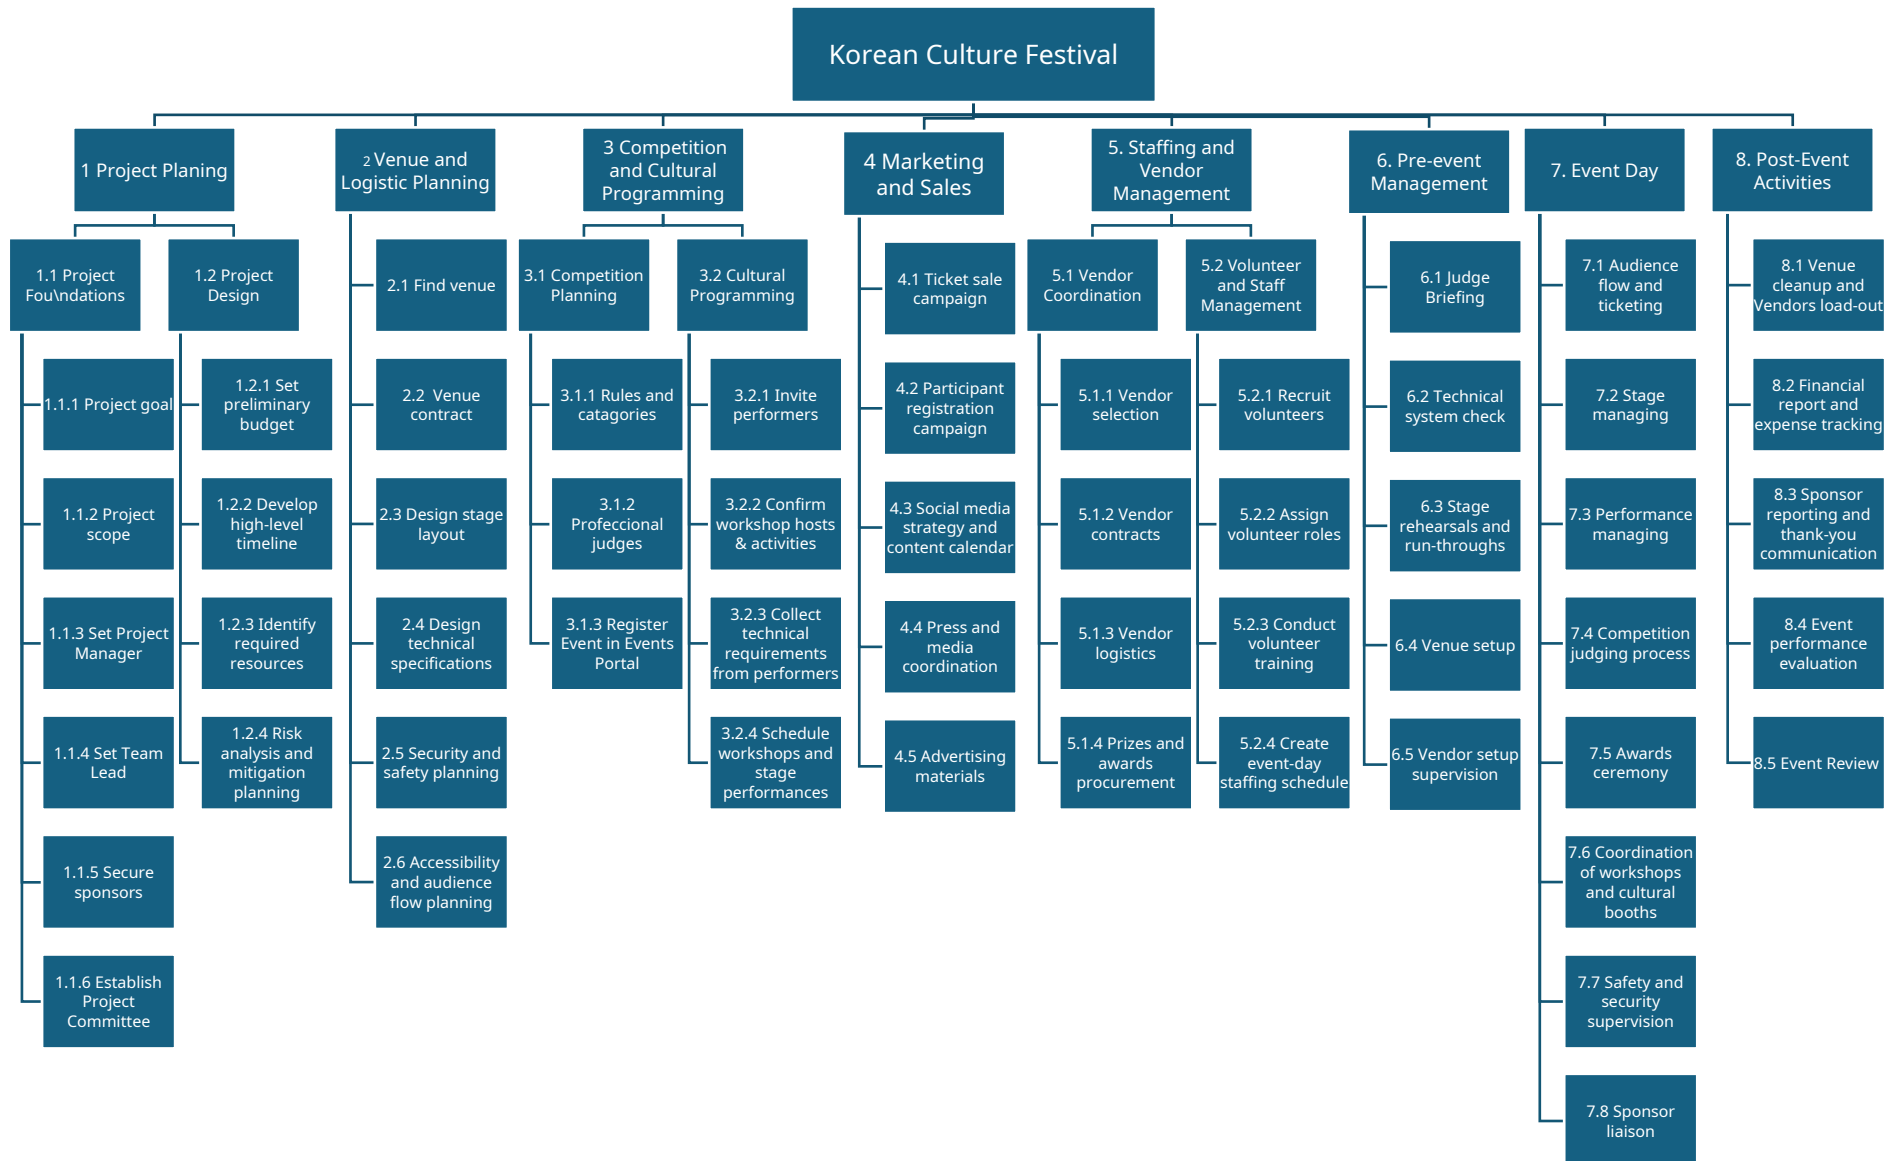

3.1. Work Breakdown Structure Overview

Korean Culture Festival

1. Project Planning

1.1 Project Foundations

1.1.1 Project goals

1.1.2 Project scope

1.1.3 Set Project Manager

1.1.4 Set Team Leads

1.1.5 Secure sponsor

1.1.6 Establish Project Committee

1.2 Project Design

1.2.1 Set preliminary budget

1.2.2 Develop high-level timeline

1.2.3 Identify required resources

1.2.4 Risk analysis and mitigation planning

2. Venue and Logistics Planning

2.1 Find Venue

2.2 Venue contract

2.3 Design stage layout

2.4 Design technical specifications

2.5 Security and safety planning

2.6 Accessibility and audience flow planning

3. Competition and Cultural Programming

3.1 Competition Planning

3.1.1 Rules and categories

3.1.2 Professional judges

3.1.3 Register Event in events portal

3.2 Cultural Programming

3.2.1 Invite performers

3.2.2 Confirm workshop hosts and activities

3.2.3 Collect technical requirements from performers

3.2.4 Schedule workshops and stage performances

4. Marketing and Sales

4.1 Ticket sales campaign

4.2 Participant registration campaign

4.3 Social media strategy and content calendar

4.4 Press and media coordination

4.5 Advertising materials

5. Staffing and Vendor Management

5.1 Vendor Coordination

5.1.1 Vendor selection

5.1.2 Vendor contracts

5.1.3 Vendor logistics

5.1.4 Prizes and awards procurement

5.2 Volunteer and Staff Management

5.2.1 Recruit volunteers

5.2.2 Assign volunteer roles

5.2.3 Conduct volunteer training

5.2.4 Create event-day staffing schedule

6. Pre-Event Operations

6.1 Judge briefing

6.2 Technical system check

6.3 Stage rehearsals and run-throughs

6.4 Venue setup

6.5 Vendor setup supervision

7. Event Day

7.1 Audience flow and ticket scanning

7.2 Stage management

7.3 Performance managing

7.4 Competition judging process

7.5 Award ceremony

7.6 Coordination of workshops and cultural booths

7.7 Safety and security supervision

7.8 Sponsor liaison

8. Post-Event Activities

8.1 Venue cleanup and vendor load-out


8.2 Financial closing and expense tracking

8.3 Sponsor reporting and thank-you communication

8.4 Event performance evaluation

8.5 Event Review

4. Organization Chart

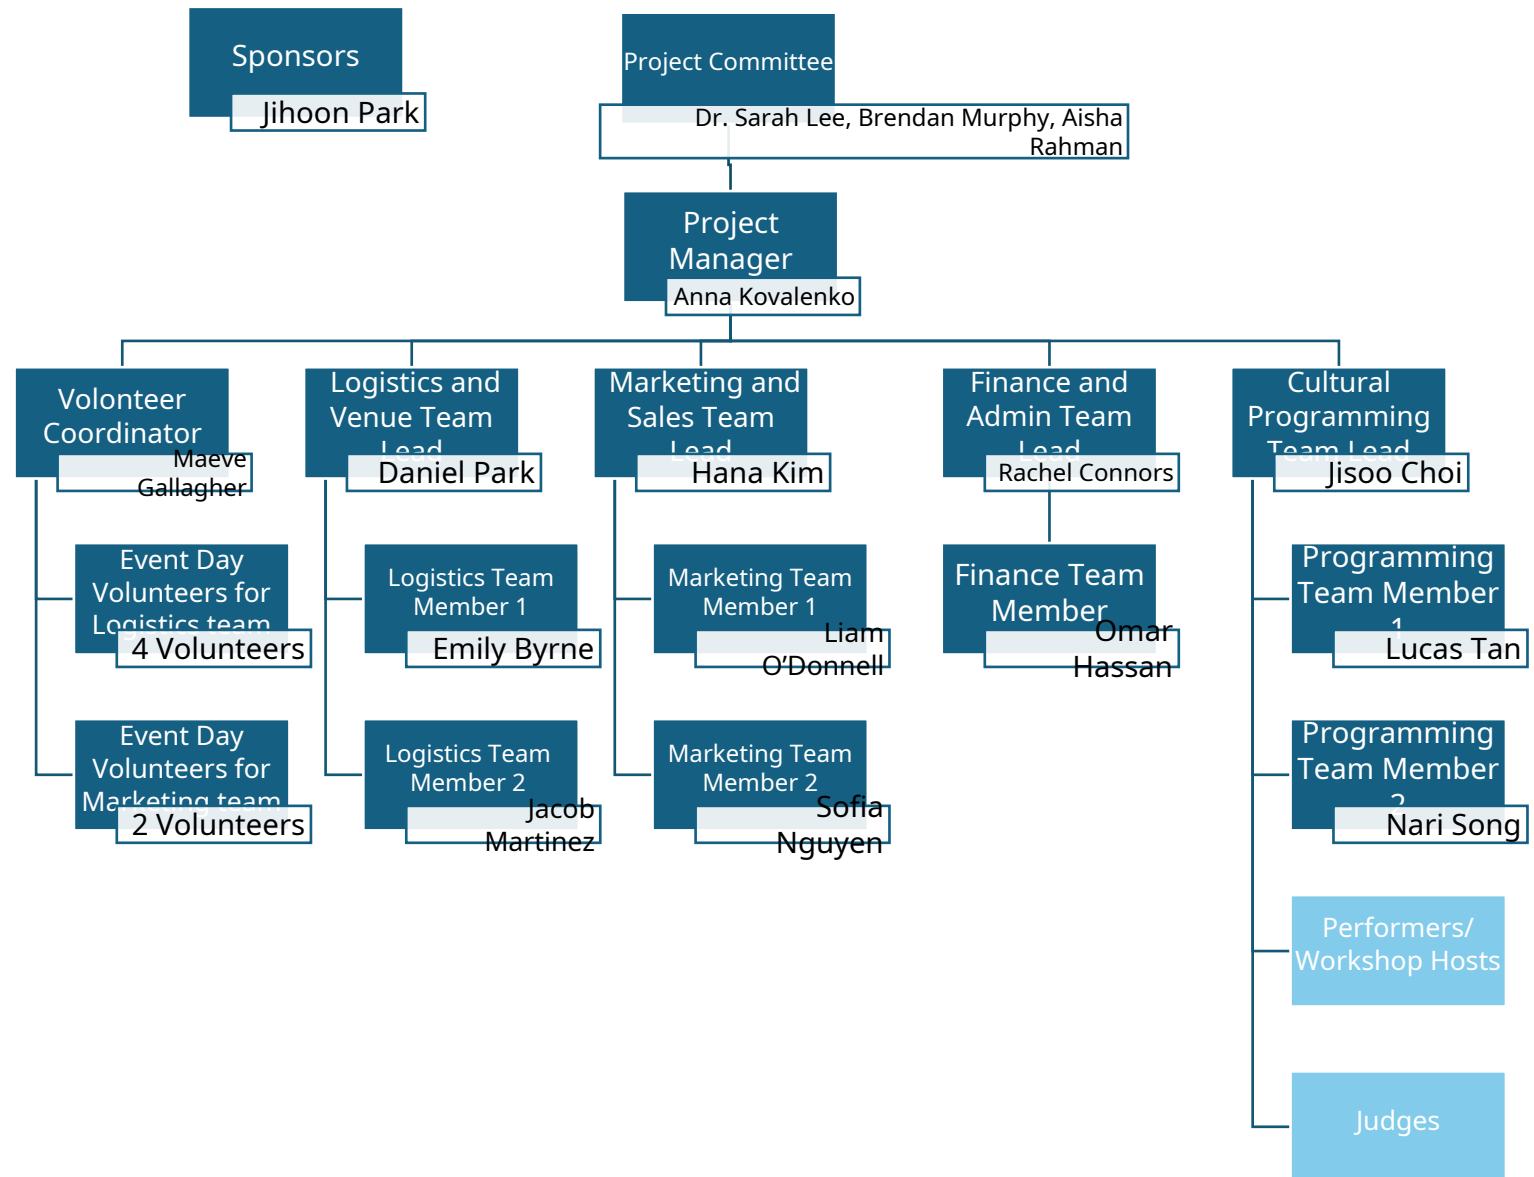

4.1. Organization Chart Overview

Sponsor: Korean Embassy in Dublin

Provides financial support, cultural guidance, and high-level oversight for the event.

Project Steering Committee

Makes strategic decisions, approves major changes, and manages escalated risks.

Project Manager (PM)

Oversees the entire project, ensuring timelines, budget, quality, and coordination across all teams.

Volunteer Coordinator

Recruits, trains, schedules, and supervises volunteers across all event areas.

Team Lead: Logistics and Venue

Manages venue setup, technical systems, safety arrangements, and all onsite operational requirements.

Team Lead: Marketing and Sales

Handles promotional campaigns, media outreach, branding, and ticket sales strategy.

Team Lead: Finance and Admin

Manages budgeting, payments, contracts, and financial reporting throughout the project.

Team Lead: Culture Programming

Develops competition rules, oversees registrations, recruits judges, and ensures fair scoring.

Event Day Volunteers

Support event operations through tasks like guest assistance, backstage coordination, and general event support.

Performers / Workshop Hosts (External)

Deliver cultural performances and interactive demonstrations such as dance, hanbok, taekwondo, and calligraphy.

Judes (External)

Submit results to the Culture Programming Lead for awards.

4.2. Organization Structure

The event will utilize a strong Matrix Organizational Structure in order to support both the ability to collaborate across teams and deliver a unified product. The Project Manager has ultimate authority over the entire event, however, each functional area (Logistics, Marketing, Finance, Programming) will have their own Team Leads who can assist the Project Manager by providing their respective area's expertise and necessary resources to successfully plan and execute the event.


A functional organizational structure is not suitable for this type of project because within a functional structure all authority is given to Department Managers and the Project Manager typically has very little authority, and therefore the communication is slow, decision making is fractured and there are numerous moving parts that need to be coordinated (performers, judges, vendors, venue logistics, etc.) for the success of the event.

Similarly, a pure Project Organizational Structure is also not suitable for this type of project, as a pure project structure would assign all employees directly to the project under the Project Manager and eliminate all functional departments. A pure project structure may work well for large, stand-alone projects, however, it would be too resource intensive for a temporary cultural event.

Hiring or reassigning permanent employees to roles that will only exist temporarily would be impractical and costly. Additionally, events like the one described often involve volunteers, part-time contributors, external performers, and contractors, which further limits the use of a pure project structure.

5. Gantt Chart

Level - 3

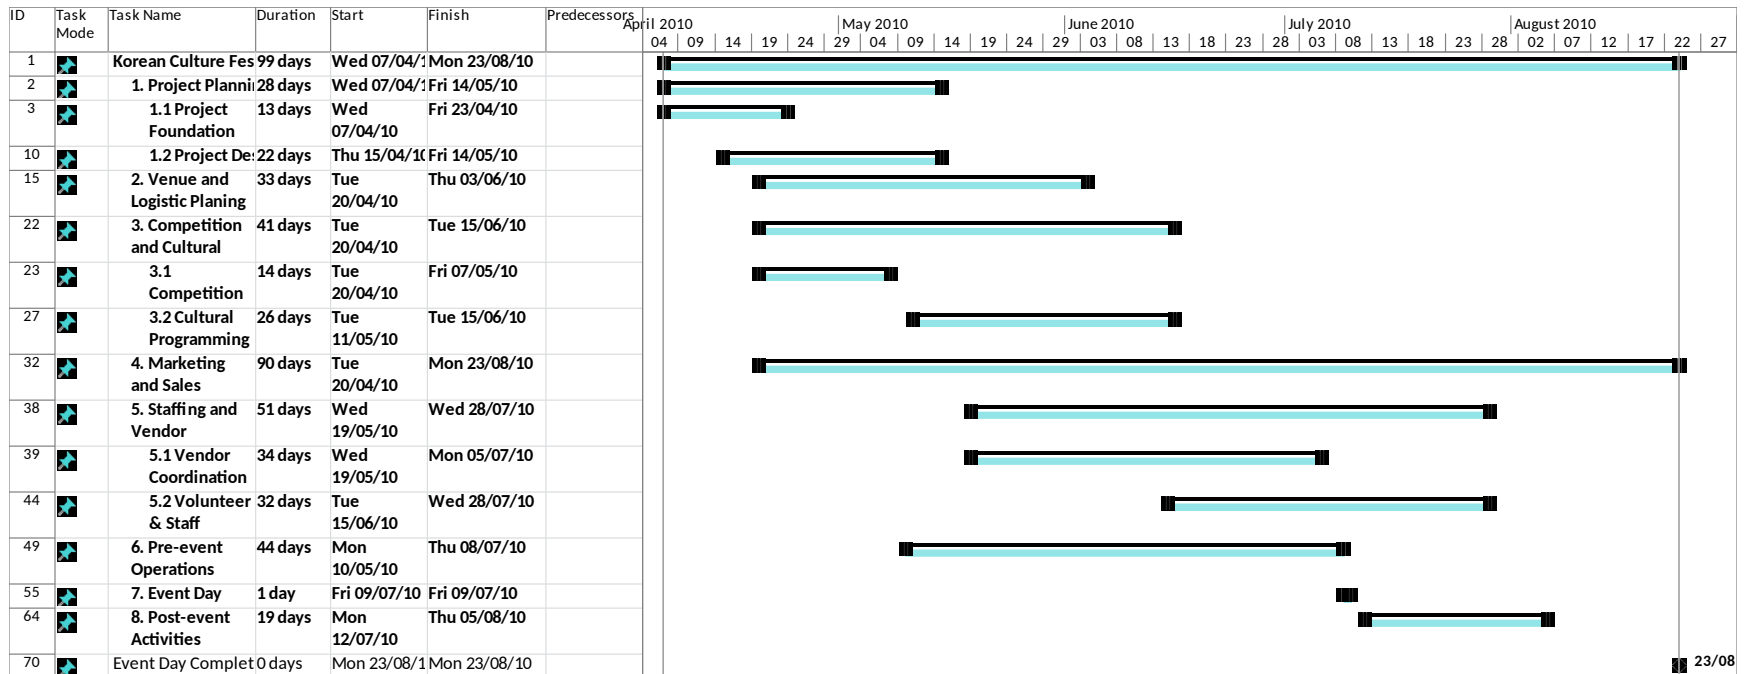

Please find full WBS in Appendix and Appendix 2.

To access Microsoft Project Gantt Chart and the Gantt Chart PDF, please use the links in Appendix 3.

6. Budget

The following table outlines the estimated budget required to deliver the Korean Culture Festival, including venue, technical setup, marketing, staffing, awards, and operational costs. All amounts are indicative and will be refined once vendor quotations and contracts are confirmed.

6.1. Project Cost Estimate

WBS Item	Units/ Hrs.	Cost/Unit/ Hr.	Subtotal (€)	WBS level 1 Total (€)	% of Total
1. Project Planning				500	4.29%
1.1 Project Foundations	25 hrs.	12.00	300		
1.2 Project Design	20 hrs.	10.00	200		
2. Venue and Logistics planning				3000	25.76%
2.2 Venue Contract	1 contract	2200.00	2,200		
2.5 Security and safety planning	1 service	500.00	500		
2.6 Accessibility and audience flow planning	10 hrs.	30.00	300		
3. Competition and Cultural Programming				2000	17.17%
3.1.2 Professional judges	4 judges	200.00	800		
3.1.3 Register Event in event portal	1 registration	50.00	50		
3.2.3 Confirm workshop hosts and activities	6 workshops	100.00	600		
3.1 Competition awards and trophies	3 lot	116.00	350		
4. Marketing and Sales				1000	8.58%
4.1 Ticket sales campaign	1 campaign	150.00	150		
4.2 Participant registration	1	100.00	100		

campaign	campaign				
4.3 Social media strategy	20 hrs.	15.00	300		
4.4 Press and media coordination	10 hrs.	20.00	200		
4.5 Advertising materials	1 lot	250.00	250		
5. Staffing and Vendor management				850	7.29%
5.1.2 Vendor contracts	1 lot	250.00	250		
5.2.3 Conduct volunteer training	3 sessions	200.00	600		
6. Pre-event Operations				2650	22.75%
6.1 Judge briefing and orientation	4hrs.	25.00	100		
6.2 Technical System check	8 hrs.	75.00	600		
6.3 Stage rehearsal and run-throughs	10 hrs.	80.00	800		
6.4 Venue setup	1 day	1150.00	1150		
8.Post-Event Activities				480	4.1%
8.1 Venue cleanup and load-out	12 hrs.	40.00	480		
Subtotal (Before Contingency)				10480	90%
Contingency (10%)				1048	10%
Total Project Cost				11528	100%

6.2. Contract Types

Project Item	Cost	Firm Fixed Price	Unit Price
1.1 Project Management	□		
1.2 Cultural Program Development			□
1.3 Venue			
Main Hall		□	
Backstage Rooms		□	
Equipment Rentals		□	
1.4 Technical Services			
Stage and AV Setup		□	
Technical Crew (Event Day)			□
1.5 Marketing			
Brochures and Printed Materials	□		
Digital Promotion	□		
Ticketing System	□		
1.6 Competition Management			
Judges			□
Competition Rules and Scoring System	□		
1.7 Performers / Workshop Hosts			□
Performer Support	□		
1.8 Volunteers and Staff			□
1.9 Vendors			
Food		□	
Merchandise		□	
1.10 Awards and Trophies		□	
1.11 Safety and Security Services		□	
1.12 Event Documentation		□	
1.13 Event Close-Out			
Financial Report	□		
Post-Event Evaluation Report	□		

6.3. Contract Types Justifications

1.1 Project Management – Cost

Description: It encompasses the provision of administrative support, the organization and control of the schedule, reporting, and liaison with stakeholders, including the Embassy.

Hours worked by the PM will usually be variable based on the project's evolving requirements. Therefore, paying for actual effort rather than using a fixed price is generally a better approach when hours will fluctuate, particularly during peak periods.

1.2 Cultural Program Development - Unit Price

Description: This includes costs related to hosting workshops for activities such as a traditional Japanese Tea Ceremony, Chinese Calligraphy, a Taekwondo demonstration, etc.

Because each host/workshop/session is paid separately, costs depend on how many workshops/sessions are booked. Therefore, Unit Price is the best method to utilize for billing purposes.

1.3.1 Venue – Main Hall - Firm Fixed Price

Description: Renting the primary venue for the entire day.

The rent for the main event space is negotiated ahead of time as a flat rate per day regardless of how much of that time is utilized or how many attendees there are.

1.3.2 Venue – Backstage Rooms - Firm Fixed Price

Description: Additional areas for performers, judges, warm-ups, and storage.

Backstage areas are also rented on a flat rate basis, and this rate remains unchanged after the contract has been finalized.

1.3.3 Venue – Equipment Rentals - Firm Fixed Price

Description: Tables, chairs, barrier systems, queuing structures, etc.

Equipment rentals are also offered as packages (i.e. "100 chairs for X Euro"), so the rental rate is established prior to delivery of the equipment.

1.4.1 Technical Services – Stage and AV Setup - Firm Fixed Price

Description: Setting up stage and audio/video equipment for events.

Technical services are contracted as complete packages. The technical setup and equipment provided under these contracts remain constant once the scope of the contract is mutually agreed upon.

1.4.2 Technical Services – Technical Crew (Event Day) - Unit Price (Hourly/Day Rate)

Description: Engineers who manage and coordinate technical aspects of events (i.e. lighting, sound, stage management), on site.

Technical staff are billed on a per hour/day basis since the amount of time they spend working at an event can vary due to rehearsal times, delays, etc.

1.5.1 Marketing – Brochures and Printed Materials – Cost

Description: Creating and distributing printed materials (posters, flyers, banners, etc.), printing, and distribution.

The costs associated with printed materials will depend on the volume of materials produced, the type of paper used, last minute reprinting of materials, and other marketing-related expenses incurred. The actual costs incurred are reimbursable.

1.5.2 Marketing – Digital Promotion - Firm Fixed Price

Description: Advertising on social media, influencer packages, and promotional content.

Digital marketing campaign packages are often packaged together into a bundle with a predetermined fixed price (e.g. a €300 Instagram ad package).

1.5.3 Marketing – Ticketing System - Firm Fixed Price

Description: Fees charged by ticketing platforms for providing the ticketing portal and/or access to the ticketing system.

Platform providers have fixed fees/package pricing or percentages; therefore, these are both considered fixed price options.

1.6.1 Competition Management – Judges - Unit Price (Per Judge)

Description: Honoring professional judges for their participation in the dance competitions.

Each judge receives a separate honorarium, along with any possible travel reimbursement. Therefore, payment is made per judge.

1.6.2 Competition Management – Competition Rules and Scoring System - Firm Fixed Price

Description: Developing scoring sheets, judging criteria, and an online registration framework.

This is a predefined deliverable that has a well-defined scope.

1.7 Performers and Workshop Hosts - Unit Price (Per Performer)

Description: Paying honoraria to performing artists, K-pop cover bands, and workshop hosts/demonstrators.

Each artist/group has a unique fee; therefore, payment is made on a per-unit basis, which is the standard practice in the entertainment industry.

1.7.1 Performers and Workshop Hosts - Performer Support – Cost

Description: Providing snacks/water/backstage necessities to performing artists.

The costs will depend on the number of performing artists and what is purchased.

1.8 Volunteers and Staff Supplies - Unit Price

Description: Purchasing volunteer identification tags/badges, volunteer shirts, and conducting training programs for volunteers.

All these items are purchased individually (by the piece/unit); therefore, the cost will depend on the number of volunteers.

1.9 Vendors – Food and Merchandise - Firm Fixed Price

Description: Each vendor pays a flat rate for booth space.

The vendor fee for renting a booth is a flat rate based on the size of the booth rented.

1.10 Awards and Trophies - Firm Fixed Price

Description: Trophy/medal/certificate awards to winning participants.

Trophies/medals/certificates are typically ordered from suppliers in quantities (flat rates) that meet the expectations of the event organizers.

1.11 Security and Safety Services - Firm Fixed Price

Description: Hiring event security personnel, managing crowds, providing medical assistance at events.

Security companies provide standardized packages for a specified number of security personnel, and the total cost is fixed.

1.12 Event Documentation (Photo and Video) - Firm Fixed Price

Description: Recording video of event highlights, award ceremonies, and workshops.

Photographers and videographers charge fixed packages (i.e. half-day, full-day).

1.13.1 Financial Close-Out – Report – Cost

Description: Producing a final report detailing financial information and expenses for the sponsors, a post-event expense audit.

The timeframe and resources required for preparing the final report may vary, depending on the project's complexity. Therefore, the actual hours/costs are reimbursed.

1.13.2 Financial Close-Out – Post-Event Evaluation Report – Cost

Description: Analysing surveys, reviewing event performance, developing recommendations for future events.

Depending on the scope of analysis requested, the scope of the analysis may expand.

7. Communications Plan

A communications plan provides a method to communicate in an efficient, timely and consistent manner with all parties associated with the event. The plan determines which communications (what), by whom (who) and through which medium (how). How often to update stakeholders also should be determined in this process. The communications plan allows event organizers to effectively coordinate with all parties, i.e., performers, vendors, judges, volunteers, etc., as well as provide a way for each party to understand how their role fits into the event's overall concept based on its cultural theme, Korea.

7.1. Communication Objectives

1. Provide all parties with appropriate information as needed and when possible.
2. Ensure that there are continuous communication and coordination among departments.
3. Assist with rapid decision making and solving problems both leading up to the event and during the event itself.
4. Create an atmosphere of openness, professionalism, and respect for others.
5. Develop a way to ensure that the cultural theme (Korea) is represented in a consistent manner throughout all communication directed toward the public.

7.2. Stakeholders and Responsibilities

Stakeholder	Role in Communication
Project Manager	Oversees communication flow; approves key updates.
Volunteer Coordinator	Communicates schedules, guidelines, and training details.
Marketing and Media Team	Handles public announcements and social media promotion.
Performers and Judges Liaison	Communicates expectations, schedules, and requirements.
Vendors Coordinator	Manages communication with vendors and marketplace partners.

Technical Team Lead	Shares technical requirements, rehearsals, and live updates.
Safety Officer	Communicates emergency procedures and incident reports.

7.3. Communication Methods

Communication Method	Purpose
Email	Formal updates, schedules, contracts, key decisions.
WhatsApp	Fast updates, last-minute changes, on-day coordination.
Zoom / Google Meet	Planning meetings and performer/judge briefings.
In-Person Meetings	Weekly organizer syncs, final rehearsal coordination.
Shared Drive (Google Drive/OneDrive)	Document sharing, schedules, maps, guides.
Social media	Public promotion is themed around Korean culture.

7.4. Meetings

Meeting Type	Scope Outline	Attendance	Frequency
Project Planning Meeting	Review project progress, update schedules, assign tasks, address risks, confirm deliverables.	Project Manager, Organizing Committee Leads (Logistics, Marketing, Technical).	Weekly (increases to twice weekly pre-event)
Volunteer Briefing	Provide training, review duties, communicate expectations, distribute event-day schedules.	Volunteer Coordinator, All Volunteers.	Two weeks before event + final rehearsal
Performer & Judges Meeting	Share competition rules, event flow, rehearsal times, stage directions, and judging guidelines.	Performers, Judges, Performer/Judge Liaison, Technical Lead.	As required + final briefing before event
Vendor Coordination Meeting	Confirm vendor setup, space allocation, arrival	Vendor Coordinator, All Registered	Weekly closer to event

	times, safety guidelines, and teardown process.	Vendors.	
Technical & Production Sync	Discuss stage setup, sound checks, lighting, equipment needs, run-throughs, and troubleshooting.	Technical Team Lead, Stage Crew, Project Manager.	Weekly. Daily during final week
Marketing & Media Meeting	Review campaign progress, social media schedule, promotional materials, cultural branding details.	Marketing Team, Social Media Manager, Project Manager.	Weekly
Event-Day Command Meeting	Final coordination, safety briefing, communication protocol, escalation procedures, station checks.	All Team Leads, Safety Officer, Project Manager.	Once (morning of the event)
Post-Event Review Meeting	Review successes, challenges, feedback scores, financial summary, and recommendations .	Project Manager, All Committee Leads.	One week after the event.

7.5. Reports

Report Name	Content Outline	Distribution List	Frequency
Project Kick-off Report	Project goals, scope overview, roles, deliverables, initial schedule, communication	Sponsor (Korean Embassy), Project Steering Committee, PM, Team Leads.	Once at project initiation

	rules.		
Project Status Report	Progress summary, completed tasks, upcoming milestones, risks/issues, action points.	Project Steering Committee, Sponsor, PM, All Team Leads.	Weekly
Budget Status Report	Current spending vs. budget, cost variances, forecasted expenses, financial risks.	PM, Finance & Admin Lead, Sponsor (as required).	Monthly Weekly near event
Risk and Issues Report	Newly identified risks, severity, mitigation actions, responsible owners, status updates.	PM, Steering Committee, Relevant Team Leads.	Weekly
Marketing Performance Report	Ticket sales updates, social media analytics, campaign effectiveness, and audience reach.	Marketing Lead, PM, Sponsor (as needed).	Weekly
Technical & Logistics Report	Venue readiness, equipment updates, vendor coordination, technical needs and risks.	Logistics Lead, Technical Team Lead, PM.	Weekly before event
Volunteer Coordination Report	Recruitment numbers, training progress, role assignments, availability issues.	Volunteer Coordinator, PM, Logistics Lead.	Weekly in final month
Project Close-Out	Final outcomes,	Sponsor, Steering	Once after event

Report	attendance metrics, financial summary, lessons learned, recommendations .	Committee, PM, Team Leads.	completion
---------------	--	-------------------------------	------------

8. Risk Analysis

No	Risk Source	Probability			Impact			Result	Impact Areas			Risk Response
		Low (1-3)	Med (4-7)	High (8-10)	Low (1-3)	Med (4-7)	High (8-10)		Cost	Sch.	Perf.	
1	Venue becomes unavailable last minute	3					10	30		X	X	Secure backup venue. Include cancellation clause in contract.
2	Technical equipment failure (sound, lighting, A/V)		5				9	45		X		Conduct full tech rehearsal. Hire on-site technicians. Keep backup equipment.
3	Low ticket sales		4				8	32	X	X		Increase marketing push Early-bird discounts Influence partnerships.
4	Not enough volunteers		5			7		35		X	X	Recruit early; create waitlist Coordinate with universities/youth

												groups.
5	Judges cancel last minute	3					9	27			X	Have two backup judges. Sign commitment contracts.
No.	Risk Source	Probability			Impact			Result	Impact Areas			Risk Response
		Low (1-3)	Med (4-7)	High (8-10)	Low (1-3)	Med (4-7)	High (8-10)	Prob. X Impact	Cost	Sch.	Perf.	
6	Performers/ workshop hosts not following schedule		6			6		36		X	X	Strict schedule briefings. Attach penalties in agreement. On-site coordinator.
7	Budget overrun		4				8	32	X			Maintain contingency reserve (10%). Weekly budget reviews.
8	Safety incident or medical emergency	2					10	20	X		X	Hire trained security. First-aid team. Emergency protocol briefing.
9	Weather-related		5			5		25			X	Provide covered

	discomfort for attendees											waiting area. Manage crowd flow efficiently.
10	Registration portal failure / technical crash		4			7		28		X	X	Test stability. Set up manual fallback registration.
11	Vendor no-show (food, merch, rentals)	3				6		18			X	Maintain backup vendor list. Confirm 48 hours before event.
No.	Risk Source	Probability			Impact			Result	Impact Areas			Risk Response
		Low (1-3)	Med (4-7)	High (8-10)	Low (1-3)	Med (4-7)	High (8-10)		Cost	Sch.	Perf.	
12	Miscommunication among teams		5			5		25		X	X	Weekly coordination meetings. Clear reporting lines. Communication plan.
13	Project goes over schedule		4				9	36	X	X		Establish detailed timeline Milestone tracking.

												Escalate delays early. Add buffer time.
--	--	--	--	--	--	--	--	--	--	--	--	---

9. Project Chapter

Project Title:	Korean Culture Festival		
Project Start Date:	April 4, 2026	Project Finish Date:	August 23, 2026
Project Manager:	Anna Kovalenko		
Project Objectives			
A successful hosting event that promotes the K-pop genre and its parent music culture in a formal atmosphere. Securing a minimum of 30 entries for the competition and achieving 80% of ticket sale capacity. High technical quality of production in respect to technical issues and equalness of the judging officers.			
Approach			
- Identify and assess a potential venue that will be best for your event, and secure the venue. - Determine how the dance competition events will take place and develop a way to communicate this information to people who are interested in participating through social media. - Set up a system for managing tickets as well as the price for tickets, where they can be purchased (ticket distribution), and monitor the sale of tickets. - Find and work with vendors. - Prepare and supervise all aspects of the event, ensuring that all necessary safety and security protocols are followed on the day of the event. - Monitor all activities after the event to ensure the venue is cleaned up and an assessment of the event has been completed.			
Roles and Responsibilities			
Name	Role	Responsibility	
Korean Embassy Dublin Representative: Minister Counsellor Jihoon Park	Sponsor	1. Provides financial support and cultural oversight. 2. Ensure the festival aligns with Korean cultural standards. 3. Approves major program elements and partnerships. 4. Acts as the official diplomatic partner for the	

		event.
Dr. Sarah Lee (Cultural Advisor) Brendan Murphy (Operations Advisor) Aisha Rahman (Community Engagement Advisor)	Project Committee	1. Provides the Project Manager with a general oversight role in managing an event from planning through to post-event. 2. Ensures cultural accuracy, safety, and quality across all event components. 3. Reviews proposals, budgets, and contracts. 4. Acts as a decision-making board for major changes.
Anna Kovalenko	Project Manager	1. Manages aspects of event management including Planning, Coordination, Execution and Evaluation. 2. Manages communication among all teams involved in the event and the Korean Embassy. 3. Manages the Event Managers met deadlines, safety protocols and quality standards. 4. Manages Risks, Escalation and Event Day Supervision.
Daniel Park	Team Lead: Logistics and Venue	1. Manages the securing of venues, finalization of layouts and management of contracts. 2. Manages the technical aspect of the event, including Sound, Light and Stage. 3. Manages Vendors (Food Stalls, Cultural Booths and

		Equipment Providers) 4. Manages the Event Day Setup, Crowd Flow, Safety and Emergency Procedures.
Emily Byrne Jacob Martinez	Logistics Team Members	1. Assist with venue preparation, booth setup, and equipment distribution. 2. Coordinate signage, seating, and backstage areas. 3. Assists Vendors with Arrival and Troubleshooting.
4 Volunteers	Event Day Volunteers for Logistics team	1. Assists with registration desks, crowd management, room guidance. 2. Support stage transitions and manage queue lines. 3. Assists with the Clean-up and Closing Procedures of the event.
Hana Kim	Team Lead: Marketing and Sales	1. Developed and implemented the Marketing Strategy for the event. 2. Manages Posters, Social Media Campaigns, Partnerships and Press Releases. 3. Manages Ticket Sales, Pricing Structure and Promotional Discounts. 4. Manages Photography/Videography and Event Branding.
Liam O'Donnell	Marketing Team	1. Produce digital content

Sofia Nguyen	Members	and manage social media accounts. 2. Design promotional materials and coordinate distribution. 3. Track ticket sales and maintain communication with attendees.
2 Volunteers	Event Day Volunteers for Marketing Team	1. Manage ticket scanning, program distribution. 2. Assist photographers and record social media content. 3. Support attendee engagement and information desks.
Rachel Connors	Team Lead: Finance and Admin	1. Manage overall event budget and financial documentation. 2. Handles vendor payments, invoices, and sponsorship funds. 3. Oversee volunteer registrations, schedules, and documentation. 4. Guarantees that All Contracts, Insurance Forms and Policies have been Completed.
Omar Hassan	Finance Team Member	1. Assists with Tracking Budget and Receipt Collection. 2. Prepares financial reports and administrative paperwork. 3. Manages volunteer sign-in and event records.
Jisoo Choi	Team Lead: Programming	1. Designs the cultural program schedule (K-pop

		performances, Hanbok booth, tea ceremony, workshops). 2. Manages Performer/Instructor/Cultural Partner Registration. 3. Guarantees Cultural Accuracy and Smooth Stage Flow. 4. Manages Backstage Operations and Performance Timing.
Lucas Tan Nari Song	Programming Team Members	1. Assist performers with preparation, call times, and backstage setup. 2. Manage props, costumes, and booth materials. 3. Support time management between performances.
Maeve Gallagher	Volunteer Coordinator	1. Manages volunteer assignments, schedules, and communication. 2. Ensures volunteers know their roles on event day. 3. Manages Breaks, Replacements and Emergency Assistance.
Performers and Workshop Hosts	External Participants	1. Registers via the Performer Portal and submits necessary details (Performance Type, Duration, Technical Requirements). 2. Follow the event schedule and arrive at the designated check-in time. 3. Comply with venue rules, safety policies, and backstage guidelines.

		4. Coordinate with the Programming Team for rehearsal time, stage cues, and setup requirements.
Judges	External Contractors	1. Evaluate performances based on established scoring criteria. 2. Guarantees Fairness, Professionalism and Cultural Integrity. 3. Submit results to the Programming Team for award announcements. 4. Must Attend Mandatory Briefing Sessions Prior to the Event.
Sign-off		
Minister Counsellor Jihoon Park Dr. Sarah Lee Brendan Murphy Aisha Rahman Anna Kovalenko Daniel Park Emily Byrne Jacob Martinez Hana Kim	Liam O'Donnell Sofia Nguyen Rachel Connors Omar Hassan Jisoo Choi Lucas Tan Nari Song Maeve Gallagher	
Comments		
• All Volunteers, Performers and Judges are required to complete a Participation Agreement prior to attending the festival. • All Staff and Volunteers will be required to review the festival's Health & Safety policies prior to the festival commencing. • A full technical rehearsal will take place prior to the commencement of the festival to ensure that all Audio, Lighting and Stage Flow requirements meet the festival's Technical Standards. • All promotional materials produced for the festival must be submitted to the Korean Embassy in Dublin for approval prior to their release to maintain Cultural Integrity. • Risk Assessments must be carried out on the layout of the Venue, Crowd Control and Technical Equipment used at the festival.		

- The festival is required to adhere to Data Protection Guidelines in respect of the collection of Participant and Ticket Holder data.
- The final program schedule must be shared with all teams at least one week before the event.
- All vendors should provide proof of insurance or compliance certificates where required.
- A contingency plan should be prepared for technical failures, performer cancellations, or delays.
- A feedback form should be distributed to participants, volunteers, and attendees to support future improvements.

10. Event Day Schedule


K-Pop Dance Competition and Korean Culture Festival

Time	Action	Description
08:00 – 09:00	Venue Opening and Technical Setup	• Technical crew arrives, sound & lighting checks begin • Stage layout finalized • Vendor stalls (food & Korean cultural booths) set up • Volunteer coordinator briefs volunteers
09:00 – 10:00	Performer and Judge Check-In	• Registration desk opens • Competing teams check in, receive badges & schedules • Judges welcomed and briefed • Backstage orientation for performers • Dressing rooms assigned
10:00 – 10:30	Opening Ceremony	• Host welcome speech • Introduction of judges • Overview of event rules • Short traditional Korean performance or cultural showcase
10:30 – 12:30	Competition Round 1	• Beginner & intermediate categories • 3–5 min per performance • Real-time scoring by judges • Volunteers manage stage transitions & timing
12:30 – 13:30	Lunch Break and Korean Culture Hour	• Food stalls open (Korean street food) • Open K-pop Random Dance Play • Cultural booths (Hangul

		writing, Korean snacks, K-beauty showcase)
13:30 – 15:00	Competition Round 2 – Advanced Category	• Advanced and group performances • Judges provide brief comments • Tech crew manages music transitions
15:00 – 15:30	Guest Performances and Workshop	• K-pop cover group performance • Dance workshop hosted by invited performers or choreographers • Audience participation encouraged
15:30 – 16:00	Judges' Deliberation	• Judges finalize scores • Staff prepares trophies, certificates, and stage for the awards ceremony
16:00 – 16:30	Awards Ceremony	• Announcement of winners (all categories) • Presentation of trophies, medals, certificates • Group photos with judges & performers
16:30 – 17:00	Closing Remarks	• Thank-you speech from the event team • Acknowledgement of sponsors, participants & volunteers • Announcement about next year's festival


Appendix

Gantt Chart Level 4 – 1. Project Planning

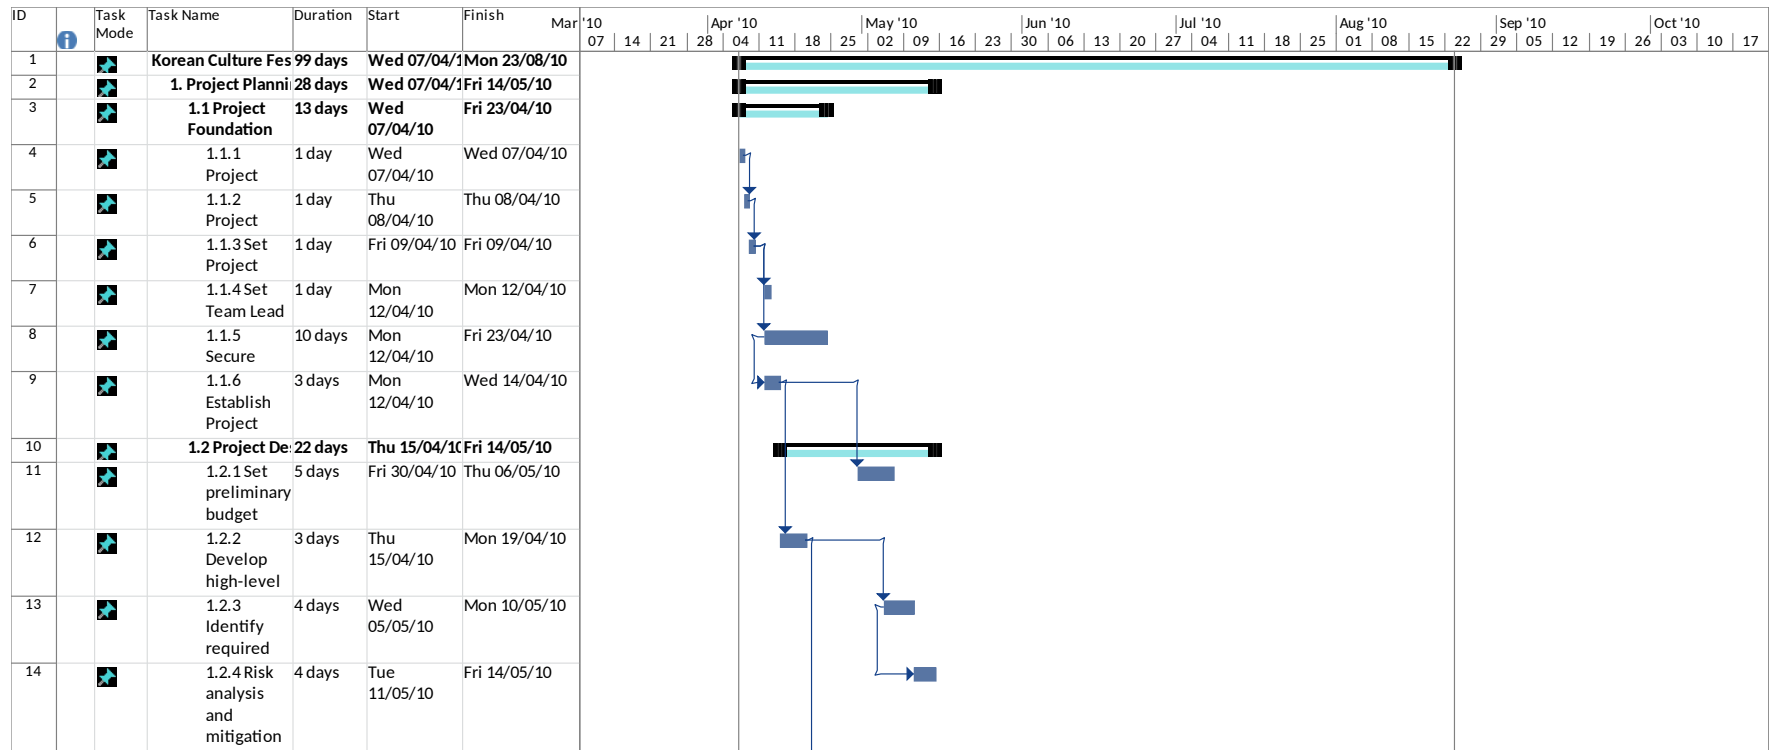


Gantt Chart Level 4 – 2. Venue and Logistic Planning

15		2. Venue and Logistic Planing	33 days	Tue 20/04/10	Thu 03/06/10
16		2.1 Find venue	14 days	Tue 20/04/10	Fri 07/05/10
17		2.2 Venue con	7 days	Mon 10/05/10	Tue 18/05/10
18		2.3 Design stage layout	5 days	Mon 10/05/10	Fri 14/05/10
19		2.4 Design technical specifications	7 days	Mon 17/05/10	Tue 25/05/10
20		2.5 Security and safety	7 days	Wed 26/05/10	Thu 03/06/10
21		2.6 Accessibility and audience	5 days	Mon 17/05/10	Fri 21/05/10




Gantt Chart Level 4 – 3. Competition and Culture

ID	Task Mode	Task Name	Duration	Start	Finish	Mar '10	Apr '10	May '10	Jun '10	Jul '10	Aug '10	Sep '10	Oct '10
22		3. Competition and Cultural	41 days	Tue 20/04/10	Tue 15/06/10								
23		3.1 Competition	14 days	Tue 20/04/10	Fri 07/05/10								
24		3.1.1 Rules and	4 days	Tue 20/04/10	Fri 23/04/10								
25		3.1.2 Professional judges	10 days	Mon 26/04/10	Fri 07/05/10								
26		3.1.3 Register Event in	2 days	Mon 26/04/10	Tue 27/04/10								
27		3.2 Cultural Programming	26 days	Tue 11/05/10	Tue 15/06/10								
28		3.2.1 Invite performers	14 days	Tue 11/05/10	Fri 28/05/10								
29		3.2.2 Confirm workshop	7 days	Mon 31/05/10	Tue 08/06/10								
30		3.2.3 Collect technical requiremer	7 days	Mon 31/05/10	Tue 08/06/10								
31		3.2.4 Schedule workshops and stage	5 days	Wed 09/06/10	Tue 15/06/10								

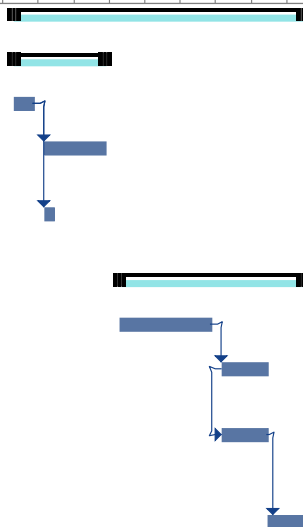


Gantt Chart Level 4 – 4. Marketing and Sales

32		4. Marketing and Sales	90 days	Tue 20/04/10	Mon 23/08/10
33		4.1 Ticket sales	60 days	Tue 20/04/10	Mon 12/07/10
34		4.2 Participant registration	40 days	Tue 20/04/10	Mon 14/06/10
35		4.3 Social media strategy and	90 days	Tue 20/04/10	Mon 23/08/10
36		4.4 Press and media coordination	30 days	Tue 20/04/10	Mon 31/05/10
37		4.5 Advertising	20 days	Mon 26/07/10	Fri 20/08/10

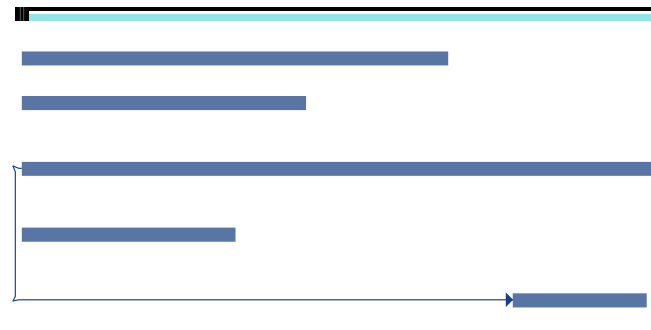


Gantt Chart Level 4 – 5. Staffing and Vendor

38		5. Staffing and Vendor	51 days	Wed 19/05/10	Wed 28/07/10
39		5.1 Vendor Coordination	34 days	Wed 19/05/10	Mon 05/07/10
40		5.1.1 Vendor	14 days	Wed 19/05/10	Mon 07/06/10
41		5.1.2 Vendor	10 days	Tue 08/06/10	Mon 21/06/10
42		5.1.3 Vendor	10 days	Tue 22/06/10	Mon 05/07/10
43		5.1.4 Prizes and awards procurement	7 days	Tue 22/06/10	Wed 30/06/10
44		5.2 Volunteer & Staff	32 days	Tue 15/06/10	Wed 28/07/10
45		5.2.1 Recruit	21 days	Tue 15/06/10	Tue 13/07/10
46		5.2.2 Assign volunteer	1 day	Wed 14/07/10	Wed 14/07/10
47		5.2.3 Conduct volunteer	7 days	Thu 15/07/10	Fri 23/07/10
48		5.2.4 Create event-day staffing	3 days	Mon 26/07/10	Wed 28/07/10

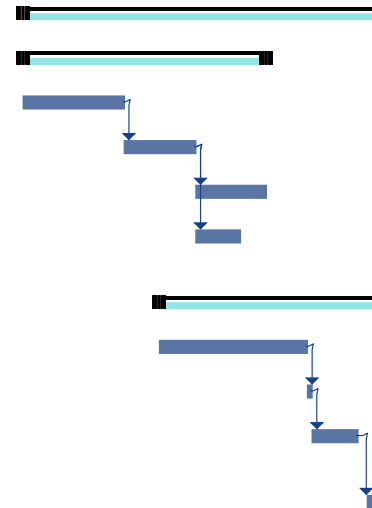


Gantt Chart Level 4 – 6. Pre-event Operations and 7. Event Day

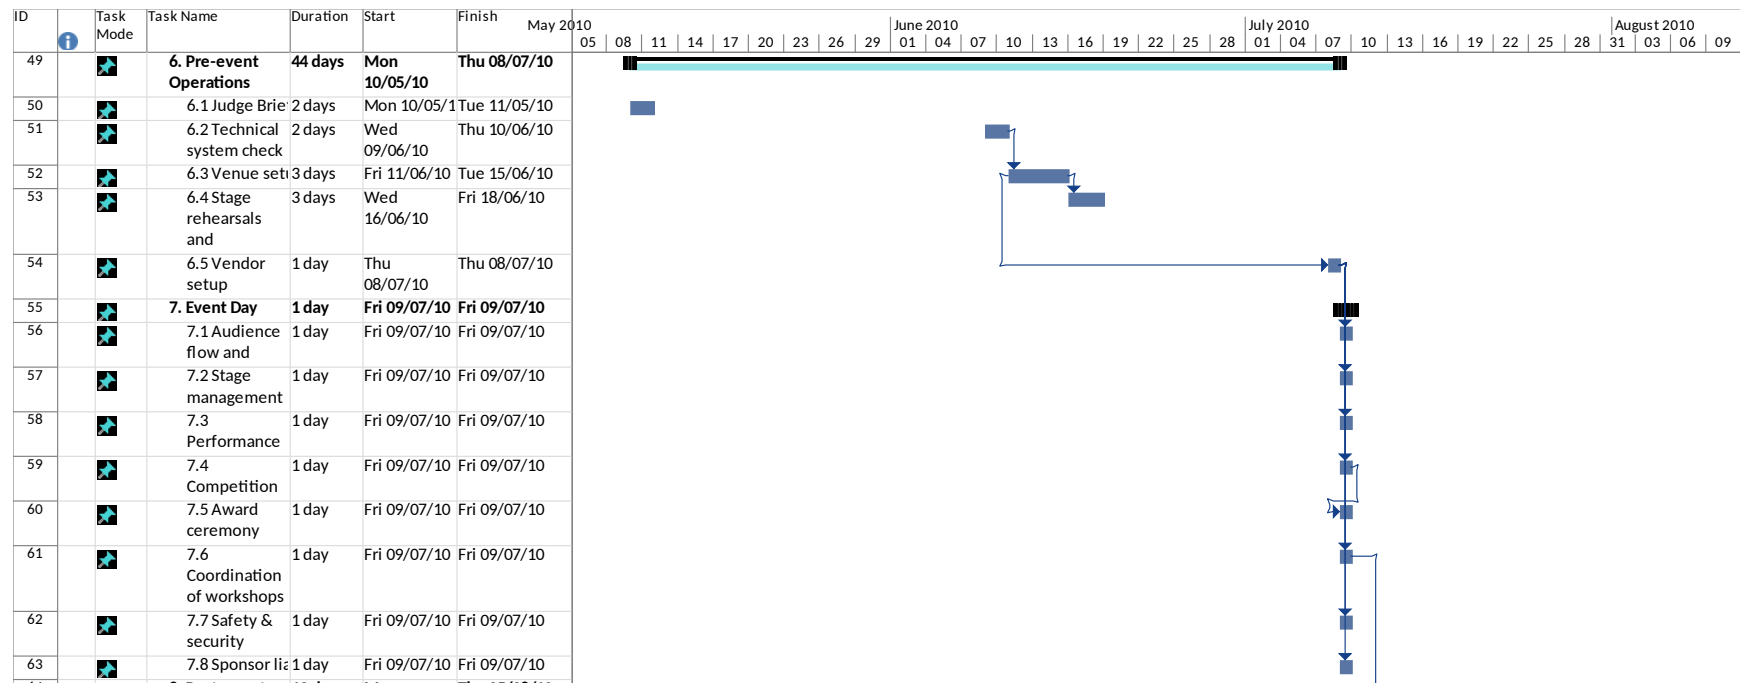


Gantt Chart Level 4 – 8. Post-event Activities


64	✚	8. Post-event Activities	19 days	Mon 12/07/10	Thu 05/08/10	
65	✚	8.1 Venue cleanup and vendor	2 days	Mon 12/07/10	Tue 13/07/10	61
66	✚	8.2 Financial closing and expense	7 days	Wed 14/07/10	Thu 22/07/10	65
67	✚	8.3 Sponsor reporting and thank-you communicatio	5 days	Wed 14/07/10	Tue 20/07/10	65
68	✚	8.4 Event performance evaluation	7 days	Fri 23/07/10	Mon 02/08/10	66
69	✚	8.5 Event Revi	3 days	Tue 03/08/10	Thu 05/08/10	68
70	✚	Event Day Complet	0 days	Mon 23/08/10	Mon 23/08/10	

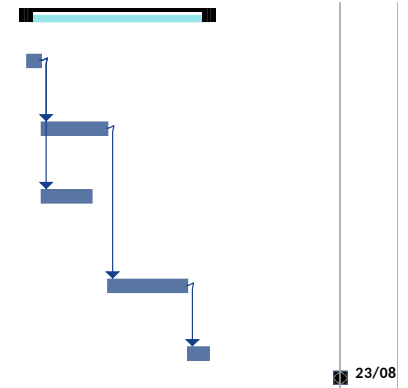

Appendix 2

Full Gantt Chart View

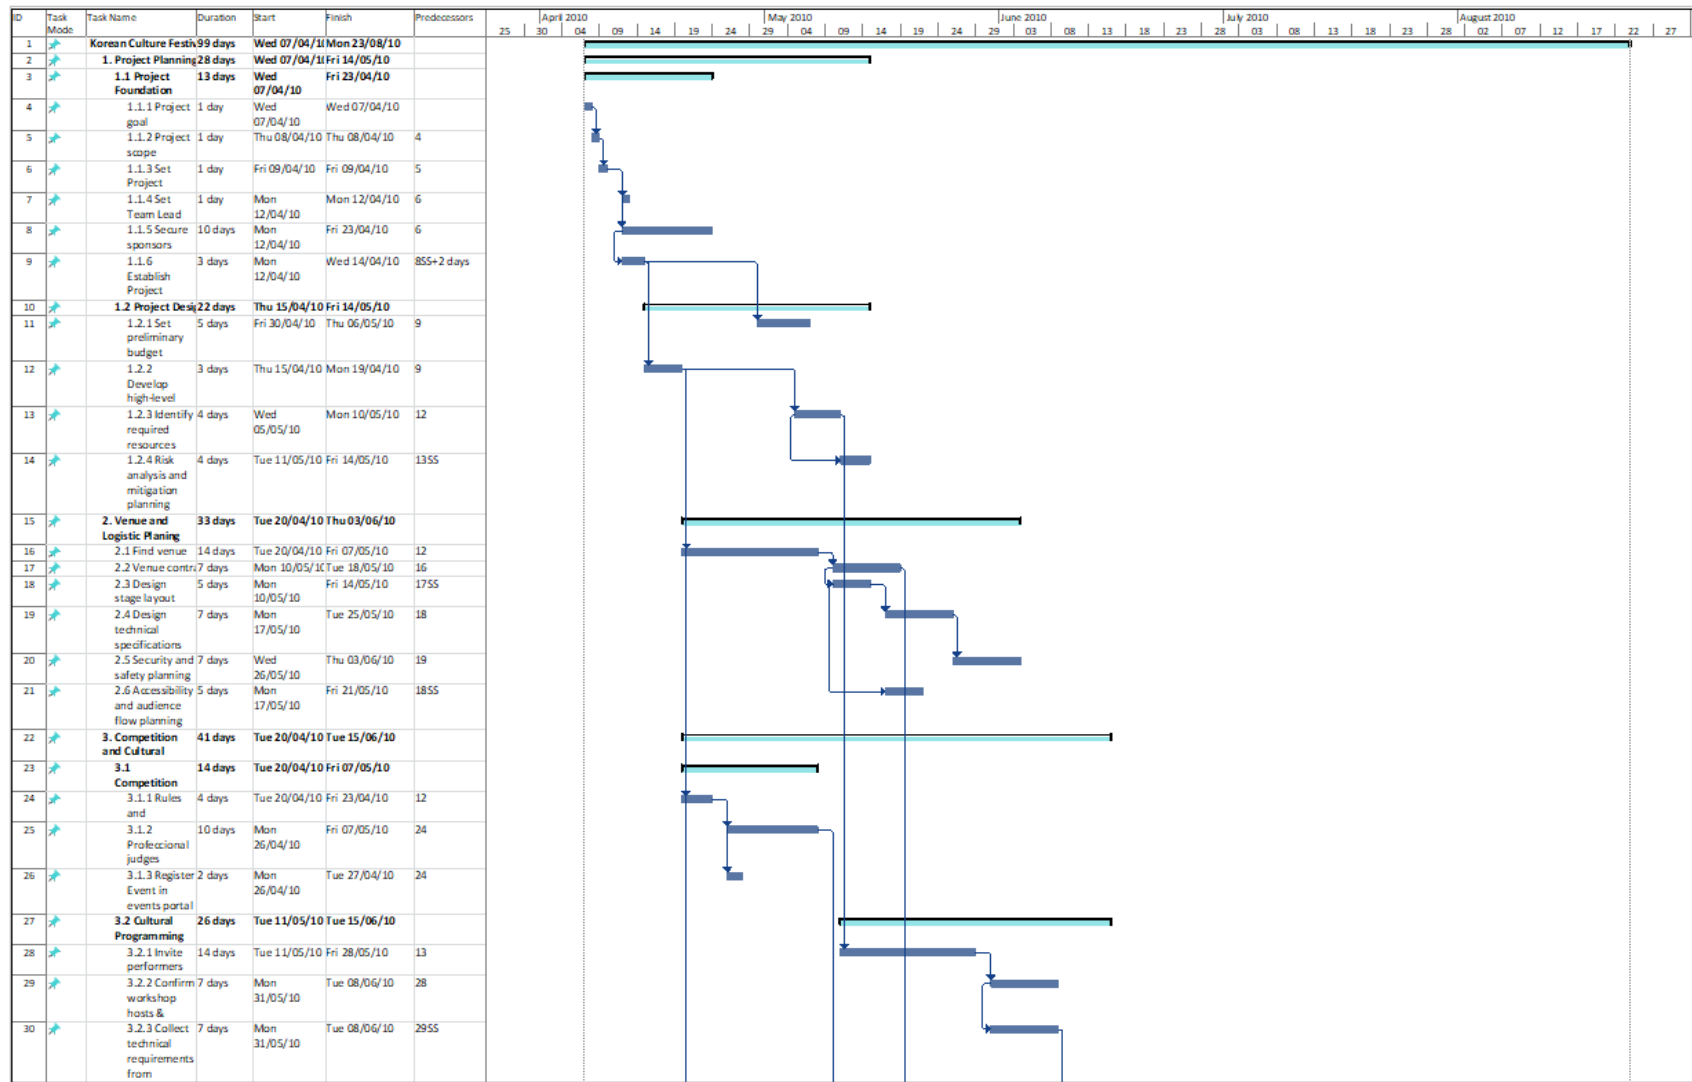

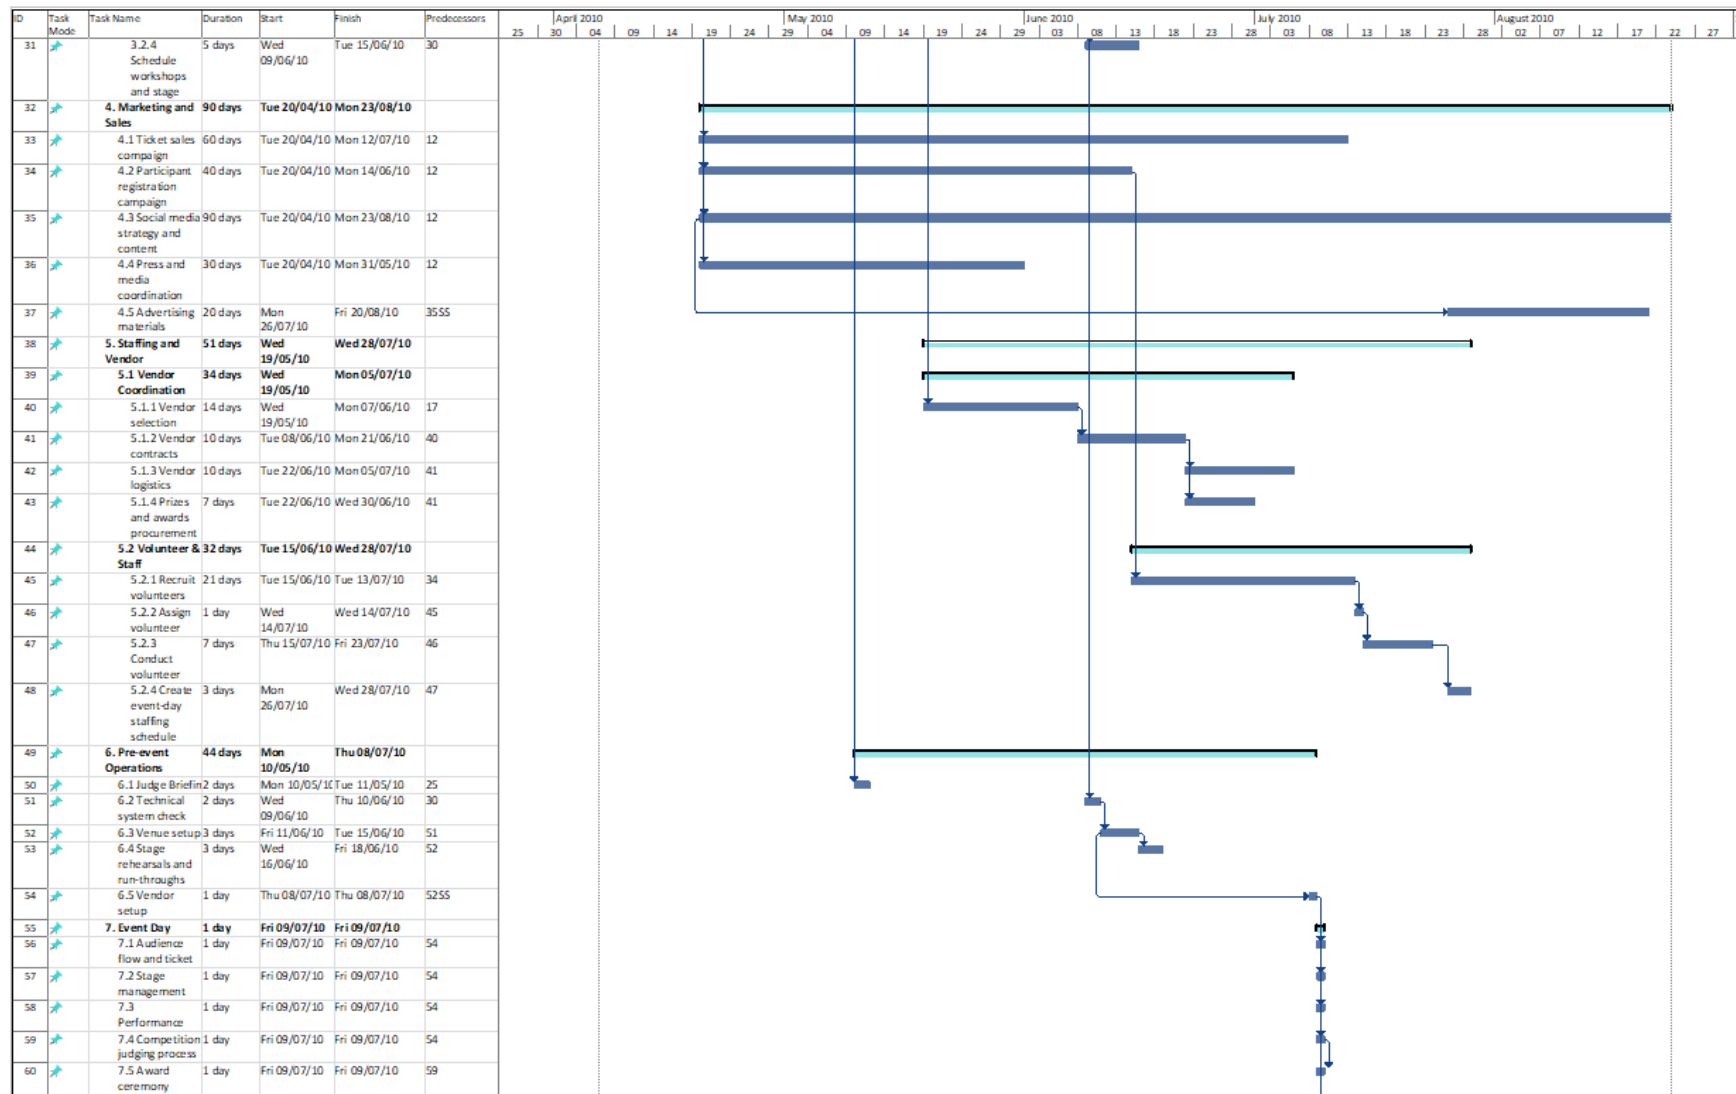



Appendix 3

Link to the Microsoft Project Gantt Chart:

https://mtuireland-my.sharepoint.com/:u:/g/personal/t00243622_mymtu_ie/IQBa4LQDB_xnSbclLC7bnJY4ASD3P60QePTOjsReR8tFRUc?email=Mairead.OSullivan%40mtu.ie&e=c0kBgf

Link to the Gantt Chart PDF:

https://mtuireland-my.sharepoint.com/:b:/g/personal/t00243622_mymtu_ie/IQDch1jy-c7HTb8_6wGuzhD2AZJyfq2L5o18w7YGJNlQm7Y?email=Mairead.OSullivan%40mtu.ie&e=feOtvZ
