


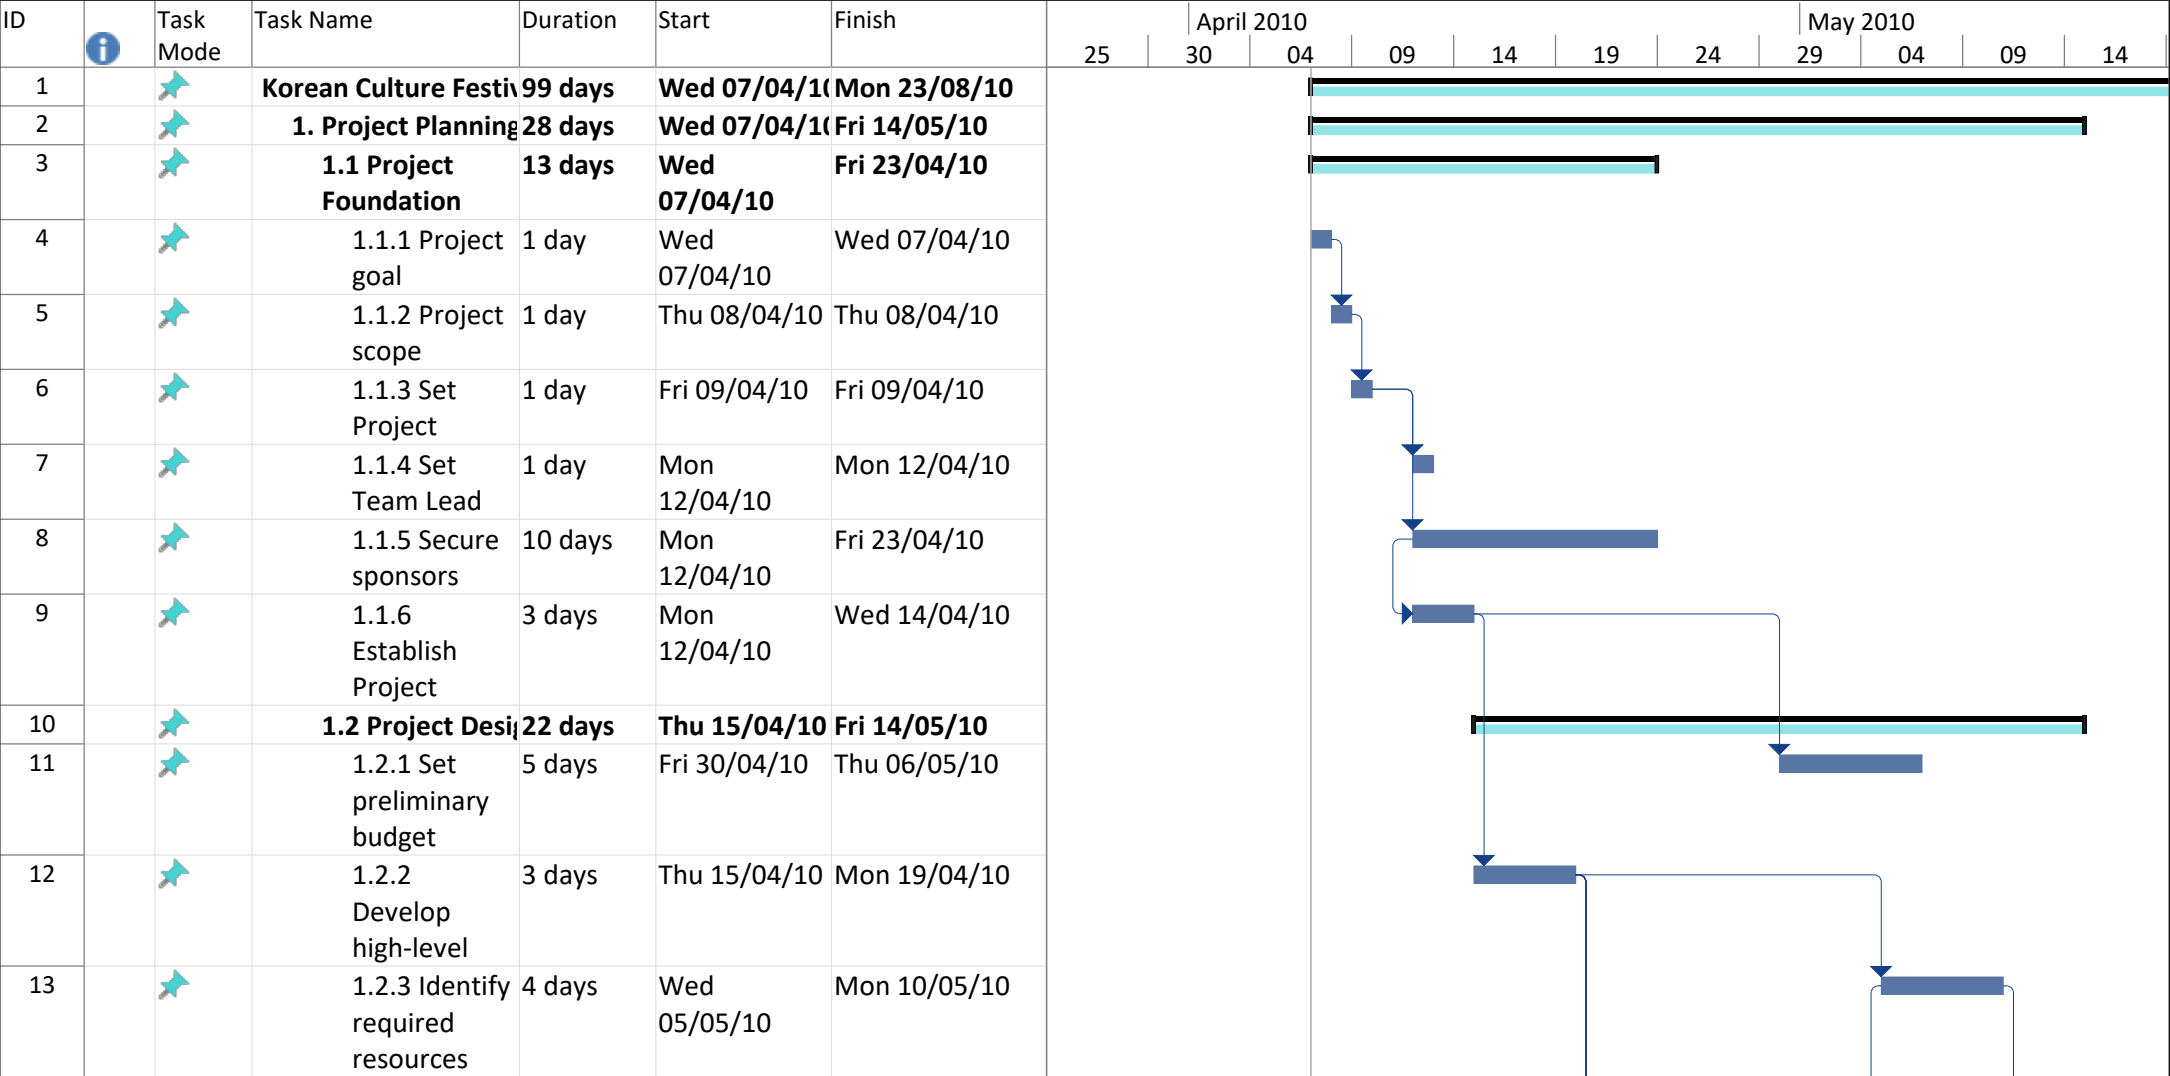

Project: msproj11  
Date: Tue 25/11/25

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary


Start-only

Finish-only

Deadline

Progress

Manual Progress

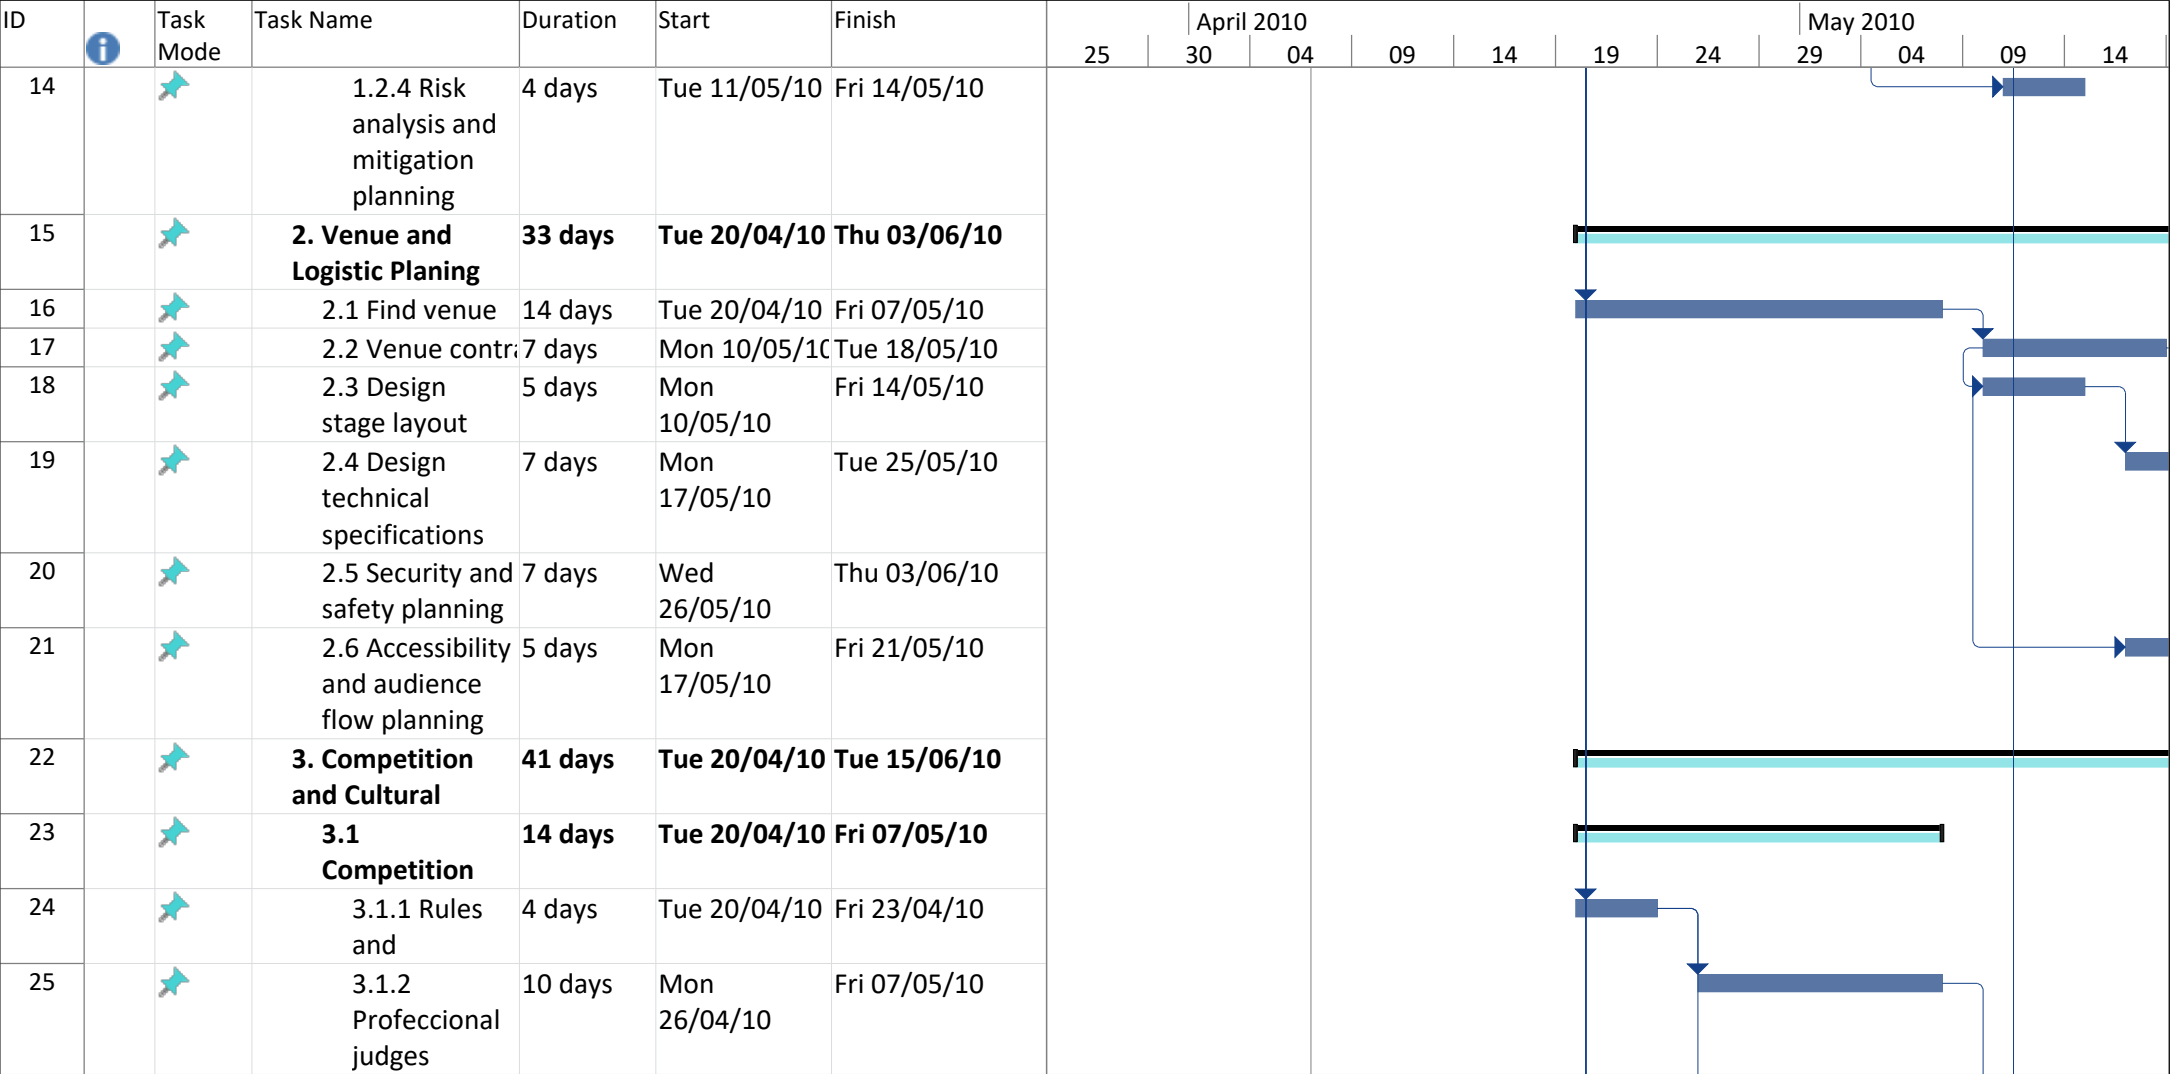

Project: msproj11  
Date: Tue 25/11/25

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

Manual Progress

Manual Summary Rollup

Manual Summary

| ID |  | Task Mode                                                                          | Task Name                                 | Duration | Start        | Finish       |    |    |    |    |    |    |    |    | May 2010 |    |    |  |
|----|--------------------------------------------------------------------------------|------------------------------------------------------------------------------------|-------------------------------------------|----------|--------------|--------------|----|----|----|----|----|----|----|----|----------|----|----|--|
|    |                                                                                |                                                                                    |                                           |          |              |              | 25 | 30 | 04 | 09 | 14 | 19 | 24 | 29 | 04       | 09 | 14 |  |
| 26 |                                                                                |    | 3.1.3 Register Event in events portal     | 2 days   | Mon 26/04/10 | Tue 27/04/10 |    |    |    |    |    |    |    |    |          |    |    |  |
| 27 |                                                                                |   | 3.2 Cultural Programming                  | 26 days  | Tue 11/05/10 | Tue 15/06/10 |    |    |    |    |    |    |    |    |          |    |    |  |
| 28 |                                                                                |   | 3.2.1 Invite performers                   | 14 days  | Tue 11/05/10 | Fri 28/05/10 |    |    |    |    |    |    |    |    |          |    |    |  |
| 29 |                                                                                |   | 3.2.2 Confirm workshop hosts &            | 7 days   | Mon 31/05/10 | Tue 08/06/10 |    |    |    |    |    |    |    |    |          |    |    |  |
| 30 |                                                                                |   | 3.2.3 Collect technical requirements from | 7 days   | Mon 31/05/10 | Tue 08/06/10 |    |    |    |    |    |    |    |    |          |    |    |  |
| 31 |                                                                                |   | 3.2.4 Schedule workshops and stage        | 5 days   | Wed 09/06/10 | Tue 15/06/10 |    |    |    |    |    |    |    |    |          |    |    |  |
| 32 |                                                                                |   | 4. Marketing and Sales                    | 90 days  | Tue 20/04/10 | Mon 23/08/10 |    |    |    |    |    |    |    |    |          |    |    |  |
| 33 |                                                                                |   | 4.1 Ticket sales campaign                 | 60 days  | Tue 20/04/10 | Mon 12/07/10 |    |    |    |    |    |    |    |    |          |    |    |  |
| 34 |                                                                                |   | 4.2 Participant registration campaign     | 40 days  | Tue 20/04/10 | Mon 14/06/10 |    |    |    |    |    |    |    |    |          |    |    |  |
| 35 |                                                                                |  | 4.3 Social media strategy and content     | 90 days  | Tue 20/04/10 | Mon 23/08/10 |    |    |    |    |    |    |    |    |          |    |    |  |

Project: msproj11

Date: Tue 25/11/25

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

Manual Progress

| ID |  | Task Mode                                                                         | Task Name                           | Duration | Start        | Finish       |    |    |    |    |    |    |    |    | April 2010 |    |    |  | May 2010 |  |  |  |
|----|--------------------------------------------------------------------------------|-----------------------------------------------------------------------------------|-------------------------------------|----------|--------------|--------------|----|----|----|----|----|----|----|----|------------|----|----|--|----------|--|--|--|
|    |                                                                                |                                                                                   |                                     |          |              |              | 25 | 30 | 04 | 09 | 14 | 19 | 24 | 29 | 04         | 09 | 14 |  |          |  |  |  |
| 36 |                                                                                |   | 4.4 Press and media coordination    | 30 days  | Tue 20/04/10 | Mon 31/05/10 |    |    |    |    |    |    |    |    |            |    |    |  |          |  |  |  |
| 37 |                                                                                |  | 4.5 Advertising materials           | 20 days  | Mon 26/07/10 | Fri 20/08/10 |    |    |    |    |    |    |    |    |            |    |    |  |          |  |  |  |
| 38 |                                                                                |  | 5. Staffing and Vendor              | 51 days  | Wed 19/05/10 | Wed 28/07/10 |    |    |    |    |    |    |    |    |            |    |    |  |          |  |  |  |
| 39 |                                                                                |  | 5.1 Vendor Coordination             | 34 days  | Wed 19/05/10 | Mon 05/07/10 |    |    |    |    |    |    |    |    |            |    |    |  |          |  |  |  |
| 40 |                                                                                |  | 5.1.1 Vendor selection              | 14 days  | Wed 19/05/10 | Mon 07/06/10 |    |    |    |    |    |    |    |    |            |    |    |  |          |  |  |  |
| 41 |                                                                                |  | 5.1.2 Vendor contracts              | 10 days  | Tue 08/06/10 | Mon 21/06/10 |    |    |    |    |    |    |    |    |            |    |    |  |          |  |  |  |
| 42 |                                                                                |  | 5.1.3 Vendor logistics              | 10 days  | Tue 22/06/10 | Mon 05/07/10 |    |    |    |    |    |    |    |    |            |    |    |  |          |  |  |  |
| 43 |                                                                                |  | 5.1.4 Prizes and awards procurement | 7 days   | Tue 22/06/10 | Wed 30/06/10 |    |    |    |    |    |    |    |    |            |    |    |  |          |  |  |  |
| 44 |                                                                                |  | 5.2 Volunteer & Staff               | 32 days  | Tue 15/06/10 | Wed 28/07/10 |    |    |    |    |    |    |    |    |            |    |    |  |          |  |  |  |
| 45 |                                                                                |  | 5.2.1 Recruit volunteers            | 21 days  | Tue 15/06/10 | Tue 13/07/10 |    |    |    |    |    |    |    |    |            |    |    |  |          |  |  |  |
| 46 |                                                                                |  | 5.2.2 Assign volunteer              | 1 day    | Wed 14/07/10 | Wed 14/07/10 |    |    |    |    |    |    |    |    |            |    |    |  |          |  |  |  |
| 47 |                                                                                |  | 5.2.3 Conduct volunteer             | 7 days   | Thu 15/07/10 | Fri 23/07/10 |    |    |    |    |    |    |    |    |            |    |    |  |          |  |  |  |

Project: msproj11

Date: Tue 25/11/25

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

Manual Progress

| ID |  Task Mode | Task Name                                | Duration       | Start               | Finish              | 25 |  | April 2010 |  | 04 |  | 09 |  | 14 |  | 19 |  | 24 |  | May 2010 |  | 29 |  | 04 |  | 09 |  | 14 |  |
|----|------------------------------------------------------------------------------------------|------------------------------------------|----------------|---------------------|---------------------|----|--|------------|--|----|--|----|--|----|--|----|--|----|--|----------|--|----|--|----|--|----|--|----|--|
|    |                                                                                          |                                          |                |                     |                     |    |  |            |  |    |  |    |  |    |  |    |  |    |  |          |  |    |  |    |  |    |  |    |  |
| 48 |          | 5.2.4 Create event-day staffing schedule | 3 days         | Mon 26/07/10        | Wed 28/07/10        |    |  |            |  |    |  |    |  |    |  |    |  |    |  |          |  |    |  |    |  |    |  |    |  |
| 49 |         | <b>6. Pre-event Operations</b>           | <b>44 days</b> | <b>Mon 10/05/10</b> | <b>Thu 08/07/10</b> |    |  |            |  |    |  |    |  |    |  |    |  |    |  |          |  |    |  |    |  |    |  |    |  |
| 50 |         | 6.1 Judge Briefin                        | 2 days         | Mon 10/05/10        | Tue 11/05/10        |    |  |            |  |    |  |    |  |    |  |    |  |    |  |          |  |    |  |    |  |    |  |    |  |
| 51 |         | 6.2 Technical system check               | 2 days         | Wed 09/06/10        | Thu 10/06/10        |    |  |            |  |    |  |    |  |    |  |    |  |    |  |          |  |    |  |    |  |    |  |    |  |
| 52 |         | 6.3 Venue setup                          | 3 days         | Fri 11/06/10        | Tue 15/06/10        |    |  |            |  |    |  |    |  |    |  |    |  |    |  |          |  |    |  |    |  |    |  |    |  |
| 53 |         | 6.4 Stage rehearsals and run-throughs    | 3 days         | Wed 16/06/10        | Fri 18/06/10        |    |  |            |  |    |  |    |  |    |  |    |  |    |  |          |  |    |  |    |  |    |  |    |  |
| 54 |         | 6.5 Vendor setup                         | 1 day          | Thu 08/07/10        | Thu 08/07/10        |    |  |            |  |    |  |    |  |    |  |    |  |    |  |          |  |    |  |    |  |    |  |    |  |
| 55 |         | <b>7. Event Day</b>                      | <b>1 day</b>   | <b>Fri 09/07/10</b> | <b>Fri 09/07/10</b> |    |  |            |  |    |  |    |  |    |  |    |  |    |  |          |  |    |  |    |  |    |  |    |  |
| 56 |         | 7.1 Audience flow and ticket             | 1 day          | Fri 09/07/10        | Fri 09/07/10        |    |  |            |  |    |  |    |  |    |  |    |  |    |  |          |  |    |  |    |  |    |  |    |  |
| 57 |         | 7.2 Stage management                     | 1 day          | Fri 09/07/10        | Fri 09/07/10        |    |  |            |  |    |  |    |  |    |  |    |  |    |  |          |  |    |  |    |  |    |  |    |  |
| 58 |         | 7.3 Performance                          | 1 day          | Fri 09/07/10        | Fri 09/07/10        |    |  |            |  |    |  |    |  |    |  |    |  |    |  |          |  |    |  |    |  |    |  |    |  |
| 59 |         | 7.4 Competition judging process          | 1 day          | Fri 09/07/10        | Fri 09/07/10        |    |  |            |  |    |  |    |  |    |  |    |  |    |  |          |  |    |  |    |  |    |  |    |  |
| 60 |         | 7.5 Award ceremony                       | 1 day          | Fri 09/07/10        | Fri 09/07/10        |    |  |            |  |    |  |    |  |    |  |    |  |    |  |          |  |    |  |    |  |    |  |    |  |

Project: msproj11

Date: Tue 25/11/25

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone















Inactive Task

Inactive Milestone


Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary















Start-only

Finish-only

Deadline

Progress

Manual Progress
















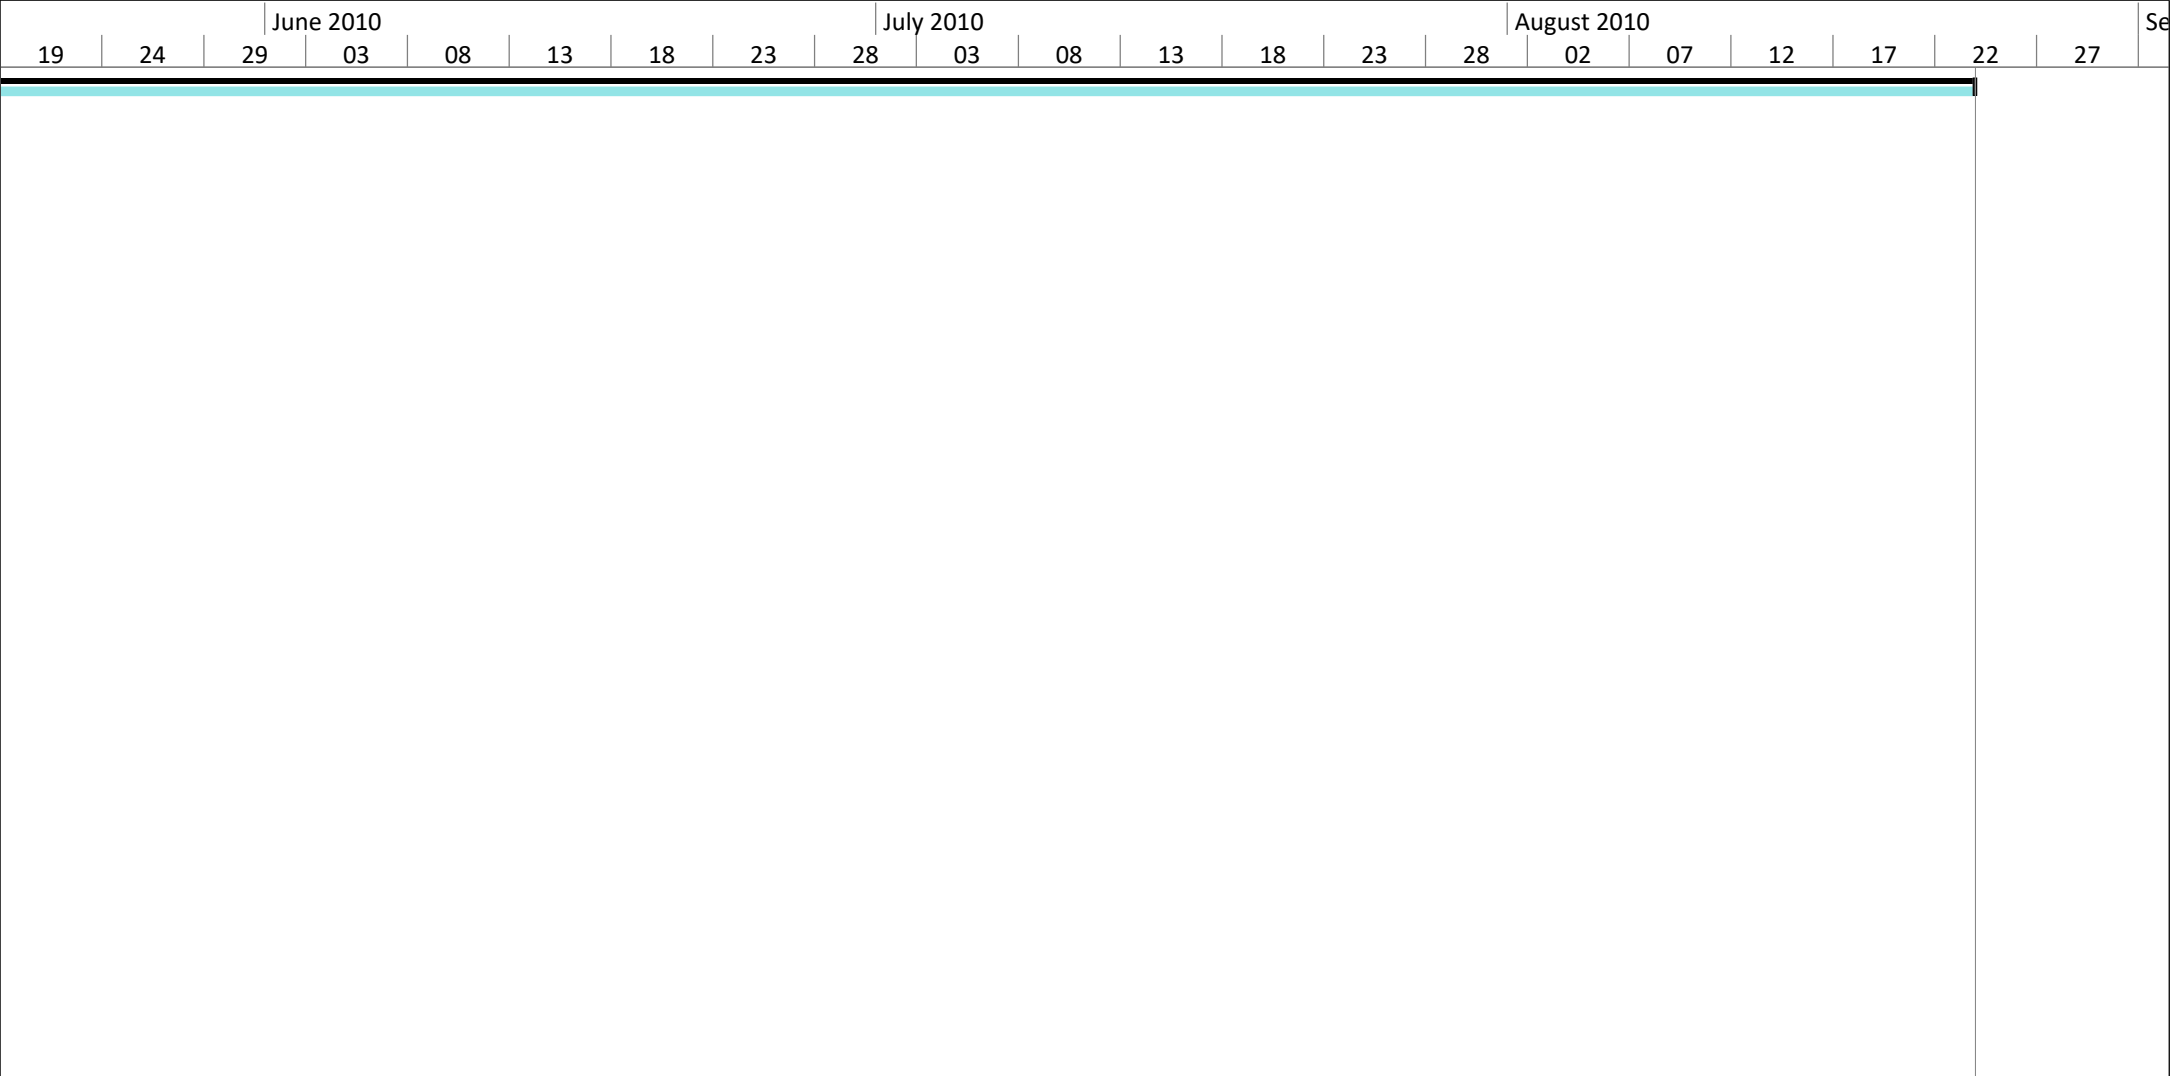


|                                         |                    |                                                                                     |                       |                                                                                       |                 |                                                                                       |
|-----------------------------------------|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|-----------------|---------------------------------------------------------------------------------------|
| Project: msproj11<br>Date: Tue 25/11/25 | Task               |  | Inactive Task         |  | Start-only      |  |
|                                         | Split              |  | Inactive Milestone    |  | Finish-only     |  |
|                                         | Milestone          |  | Inactive Summary      |  | Deadline        |  |
|                                         | Summary            |  | Manual Task           |  | Progress        |  |
|                                         | Project Summary    |  | Duration-only         |  | Manual Progress |  |
|                                         | External Tasks     |  | Manual Summary Rollup |  |                 |                                                                                       |
|                                         | External Milestone |  | Manual Summary        |  |                 |                                                                                       |

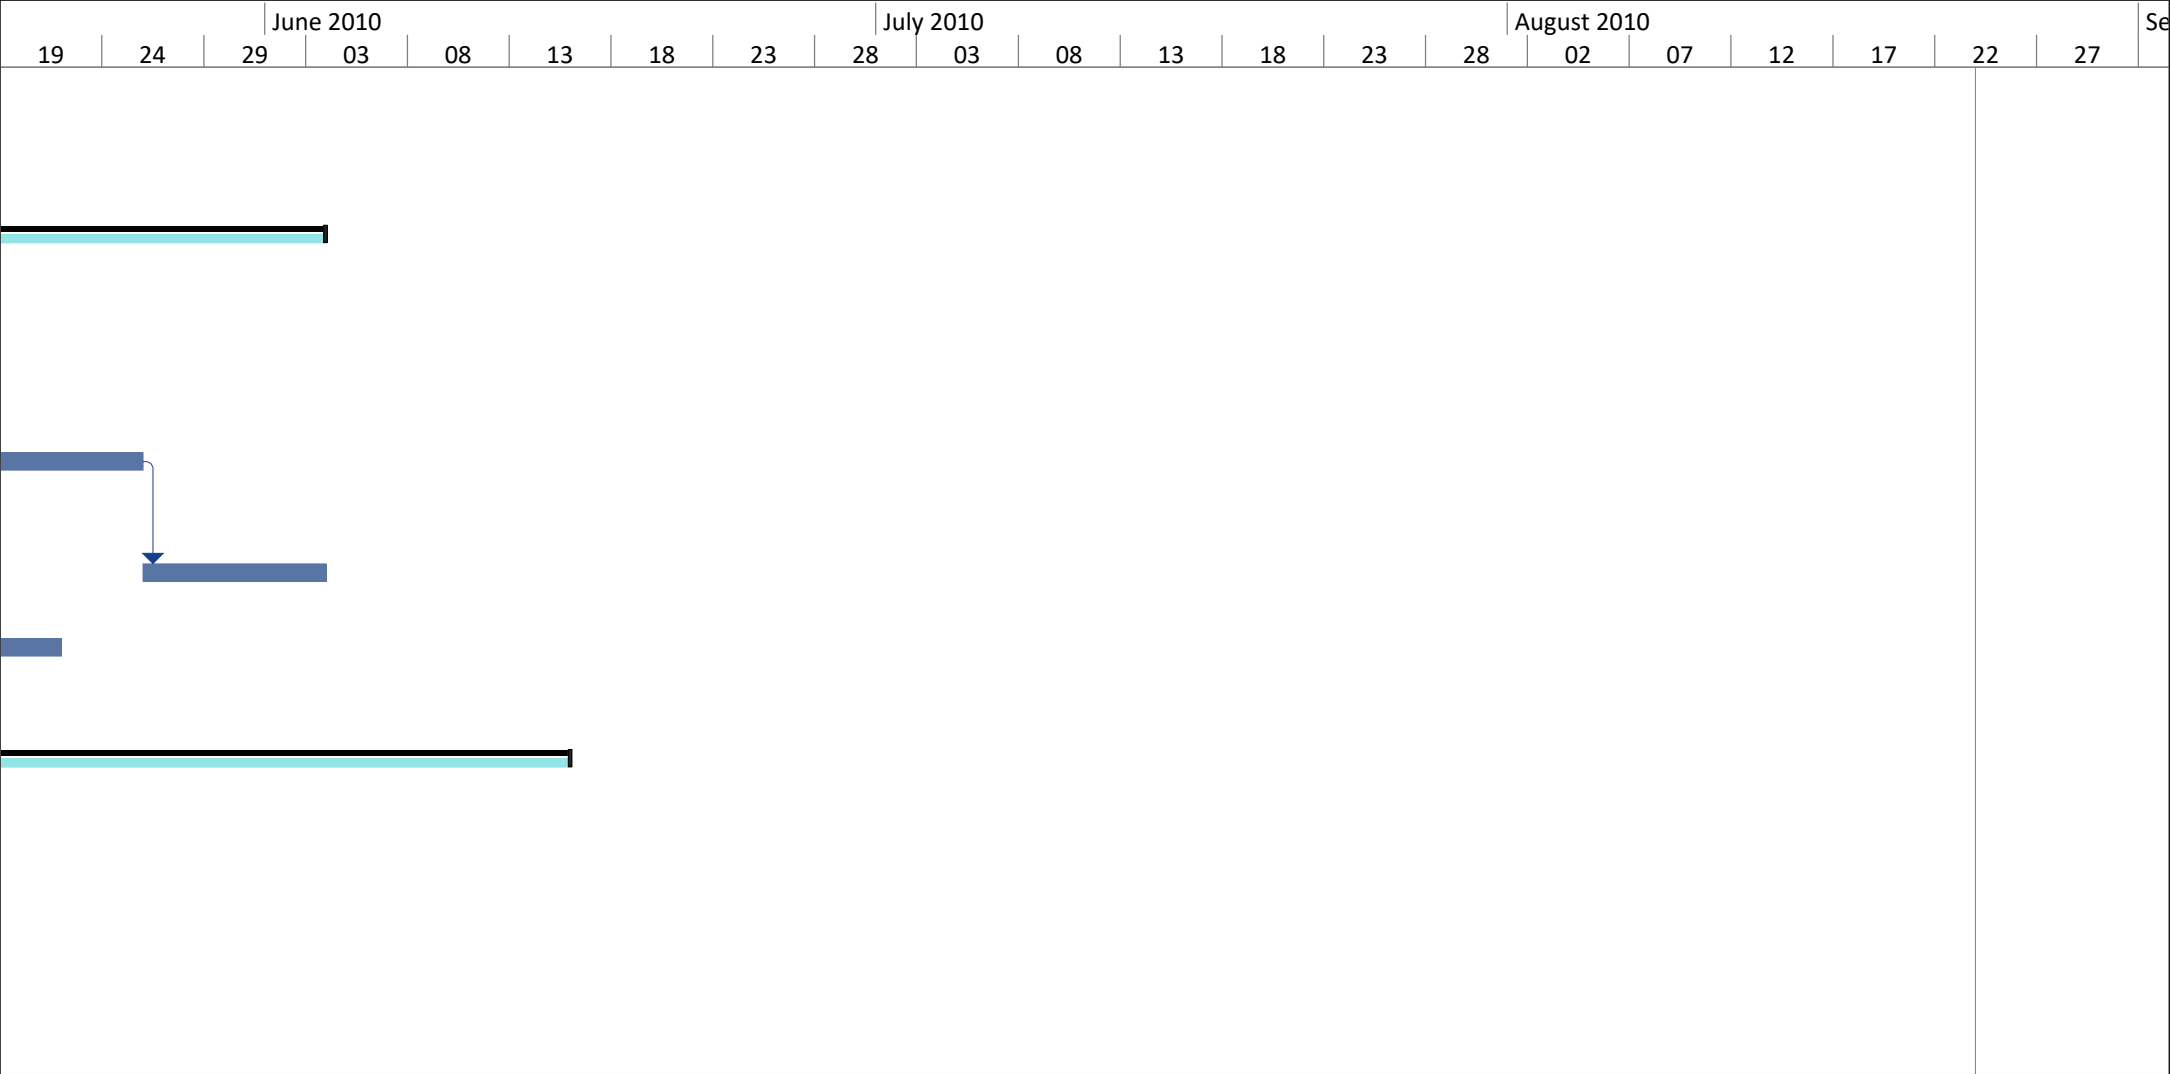

|                                         |                    |  |                       |  |                 |  |
|-----------------------------------------|--------------------|--|-----------------------|--|-----------------|--|
| Project: msproj11<br>Date: Tue 25/11/25 | Task               |  | Inactive Task         |  | Start-only      |  |
|                                         | Split              |  | Inactive Milestone    |  | Finish-only     |  |
|                                         | Milestone          |  | Inactive Summary      |  | Deadline        |  |
|                                         | Summary            |  | Manual Task           |  | Progress        |  |
|                                         | Project Summary    |  | Duration-only         |  | Manual Progress |  |
|                                         | External Tasks     |  | Manual Summary Rollup |  |                 |  |
|                                         | External Milestone |  | Manual Summary        |  |                 |  |







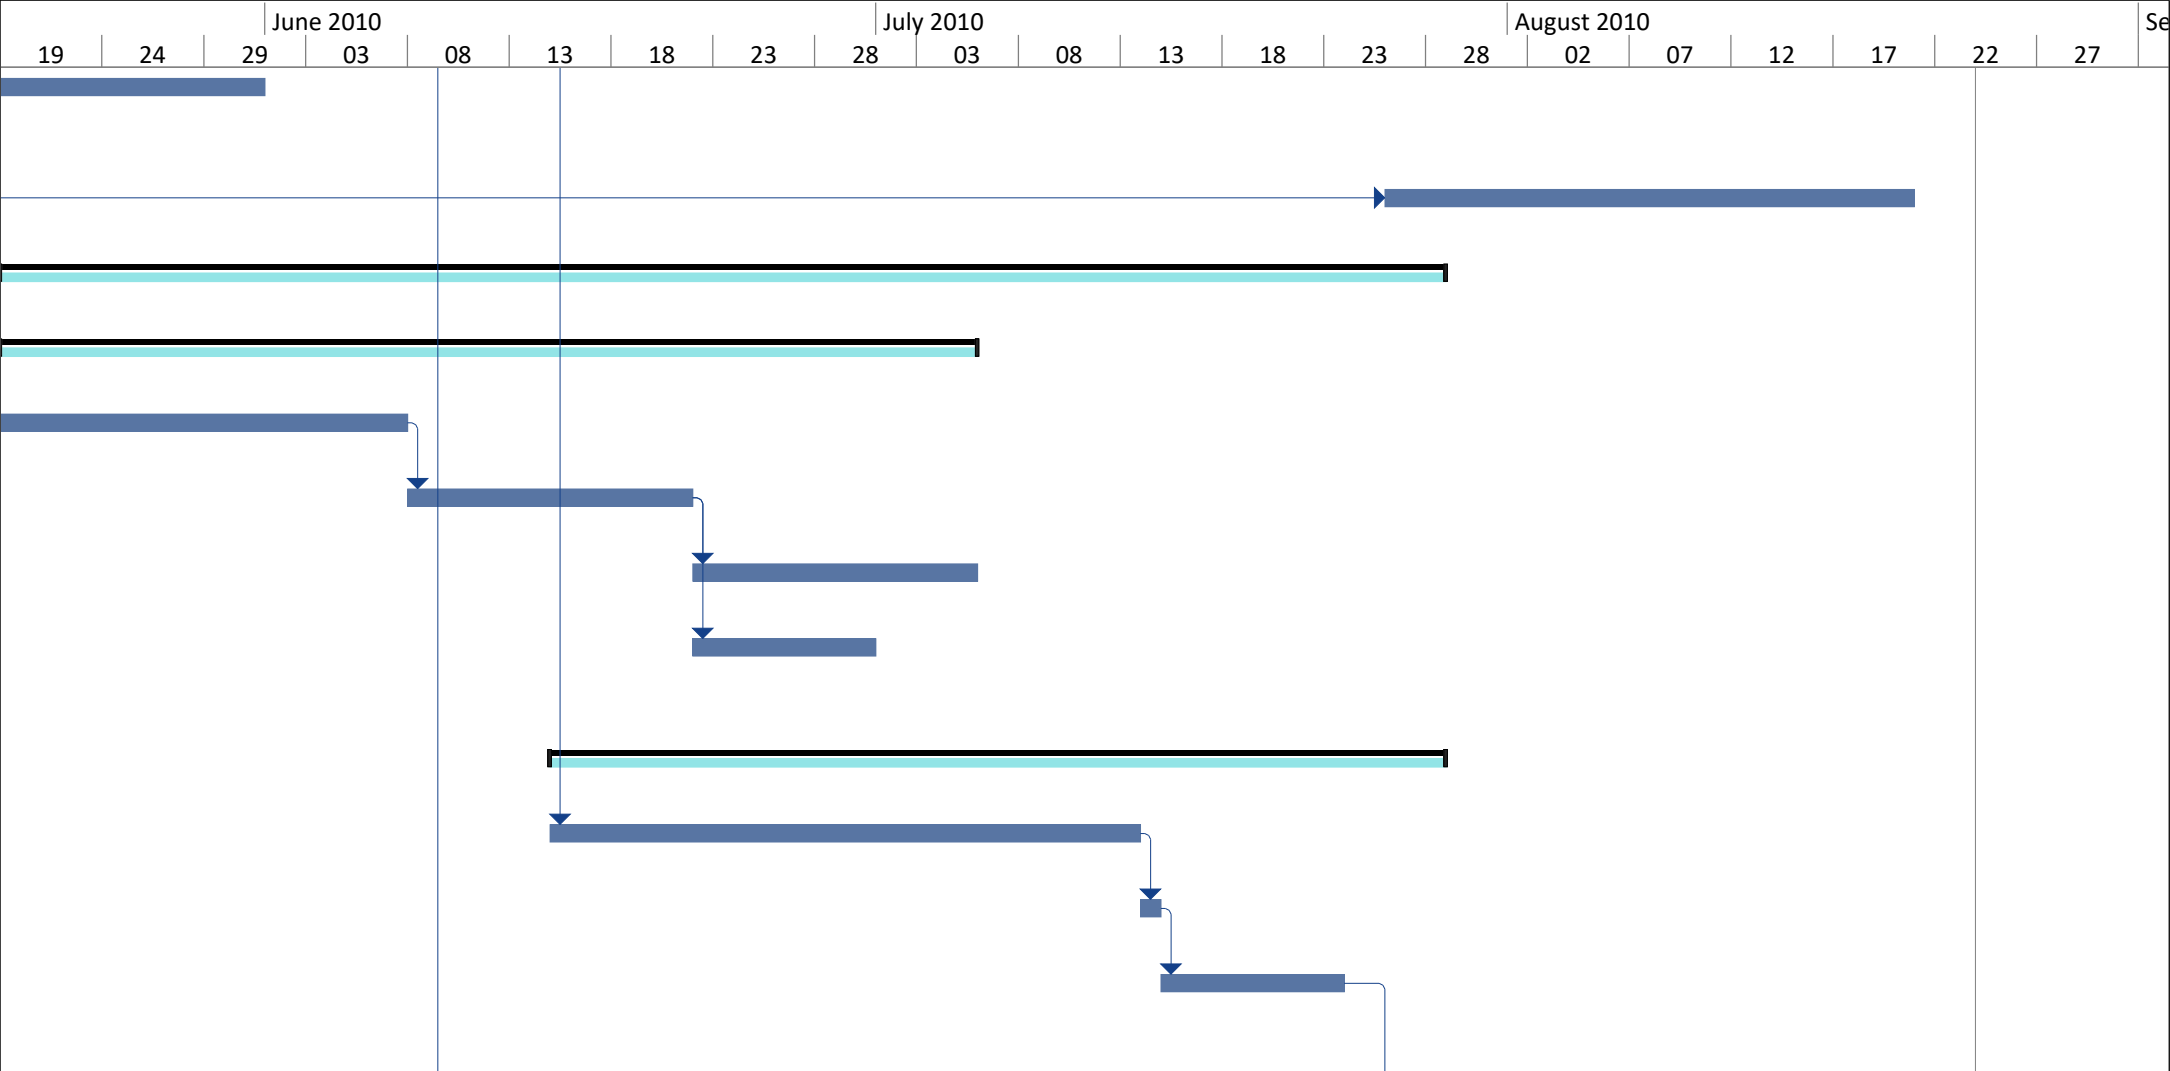


Project: msproj11  
Date: Tue 25/11/25

|                    |                                                                                     |                       |                                                                                       |                 |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|-----------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Task         |  | Start-only      |  |
| Split              |  | Inactive Milestone    |  | Finish-only     |  |
| Milestone          |  | Inactive Summary      |  | Deadline        |  |
| Summary            |  | Manual Task           |  | Progress        |  |
| Project Summary    |  | Duration-only         |  | Manual Progress |  |
| External Tasks     |  | Manual Summary Rollup |  |                 |                                                                                       |
| External Milestone |  | Manual Summary        |  |                 |                                                                                       |

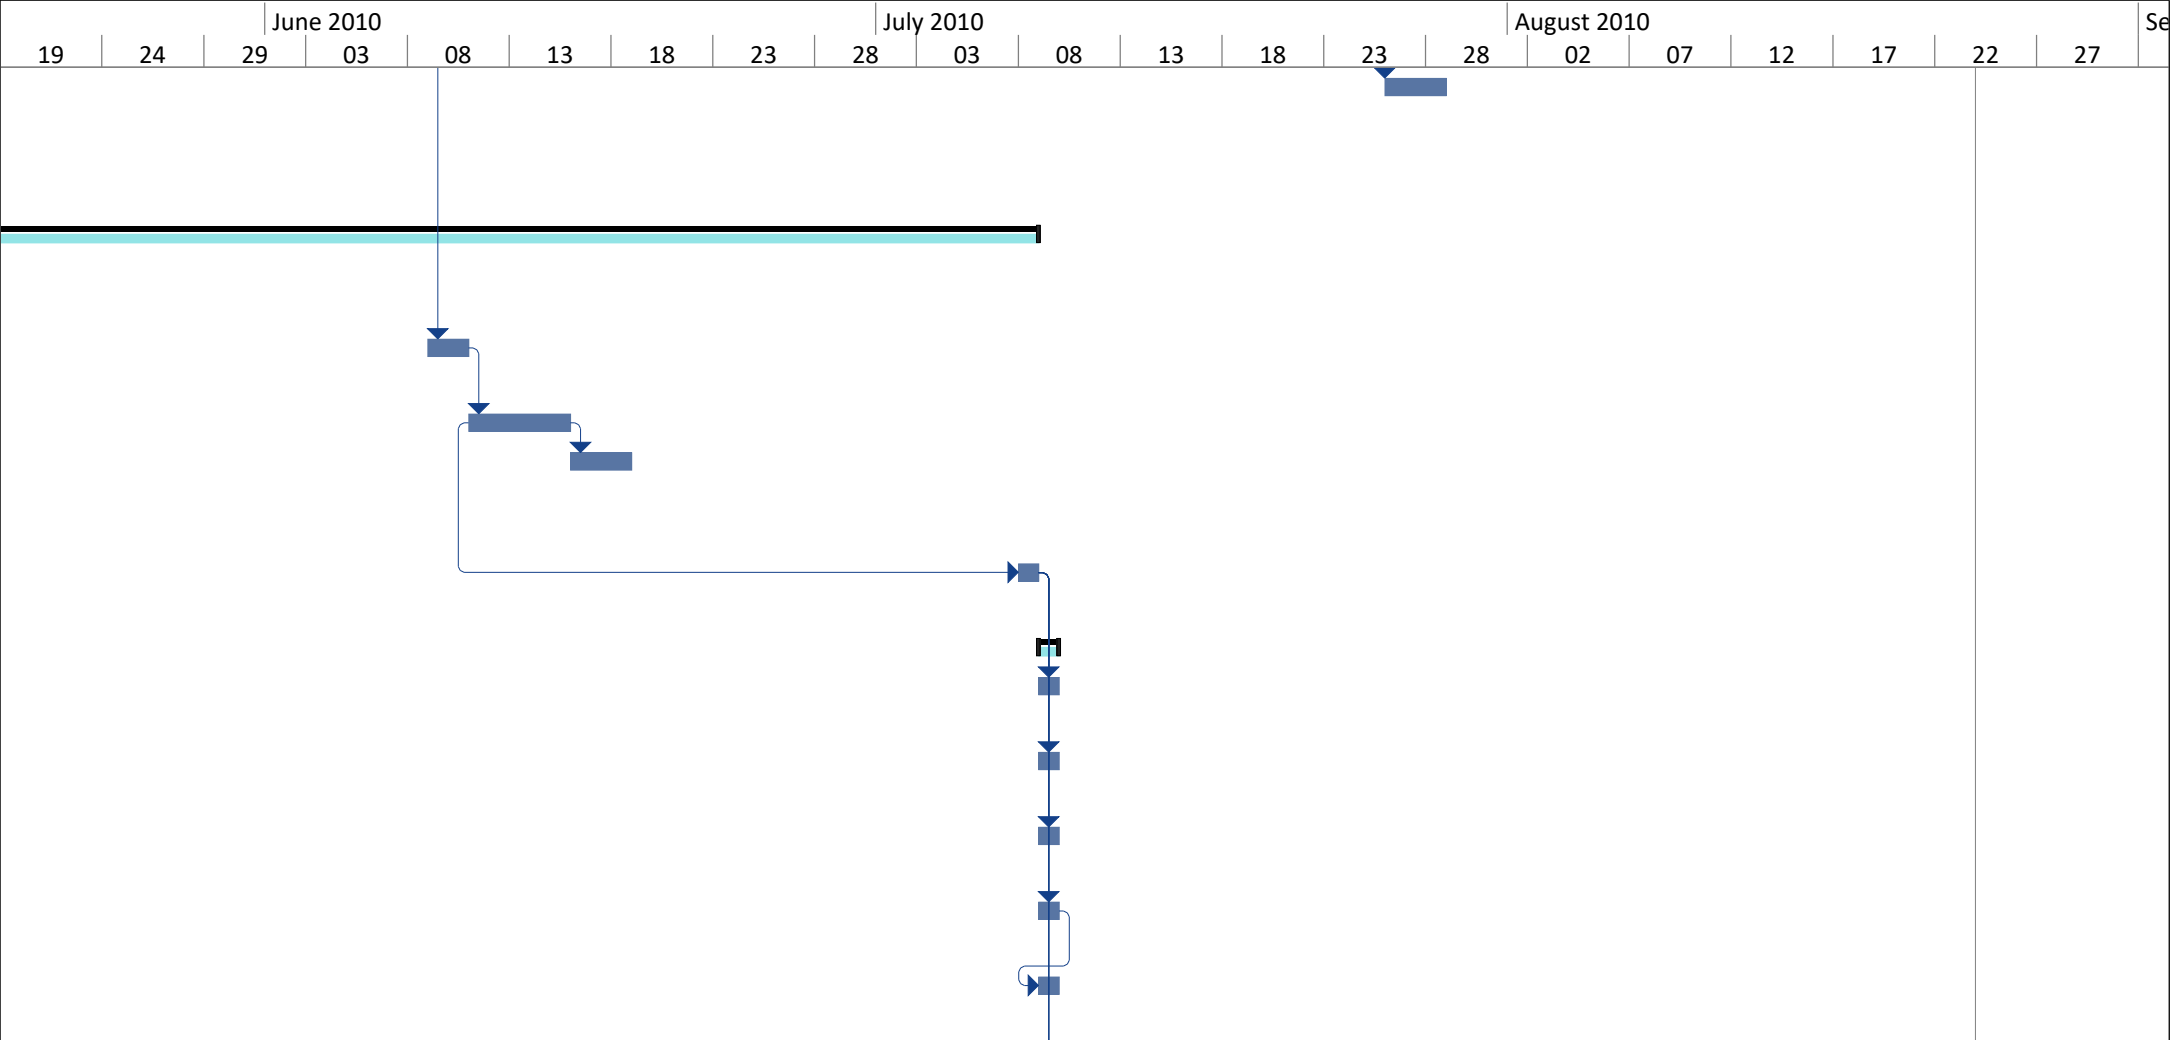

|                                         |                    |                                                                                     |                       |                                                                                       |                 |                                                                                       |
|-----------------------------------------|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|-----------------|---------------------------------------------------------------------------------------|
| Project: msproj11<br>Date: Tue 25/11/25 | Task               |  | Inactive Task         |  | Start-only      |  |
|                                         | Split              |  | Inactive Milestone    |  | Finish-only     |  |
|                                         | Milestone          |  | Inactive Summary      |  | Deadline        |  |
|                                         | Summary            |  | Manual Task           |  | Progress        |  |
|                                         | Project Summary    |  | Duration-only         |  | Manual Progress |  |
|                                         | External Tasks     |  | Manual Summary Rollup |  |                 |                                                                                       |
|                                         | External Milestone |  | Manual Summary        |  |                 |                                                                                       |

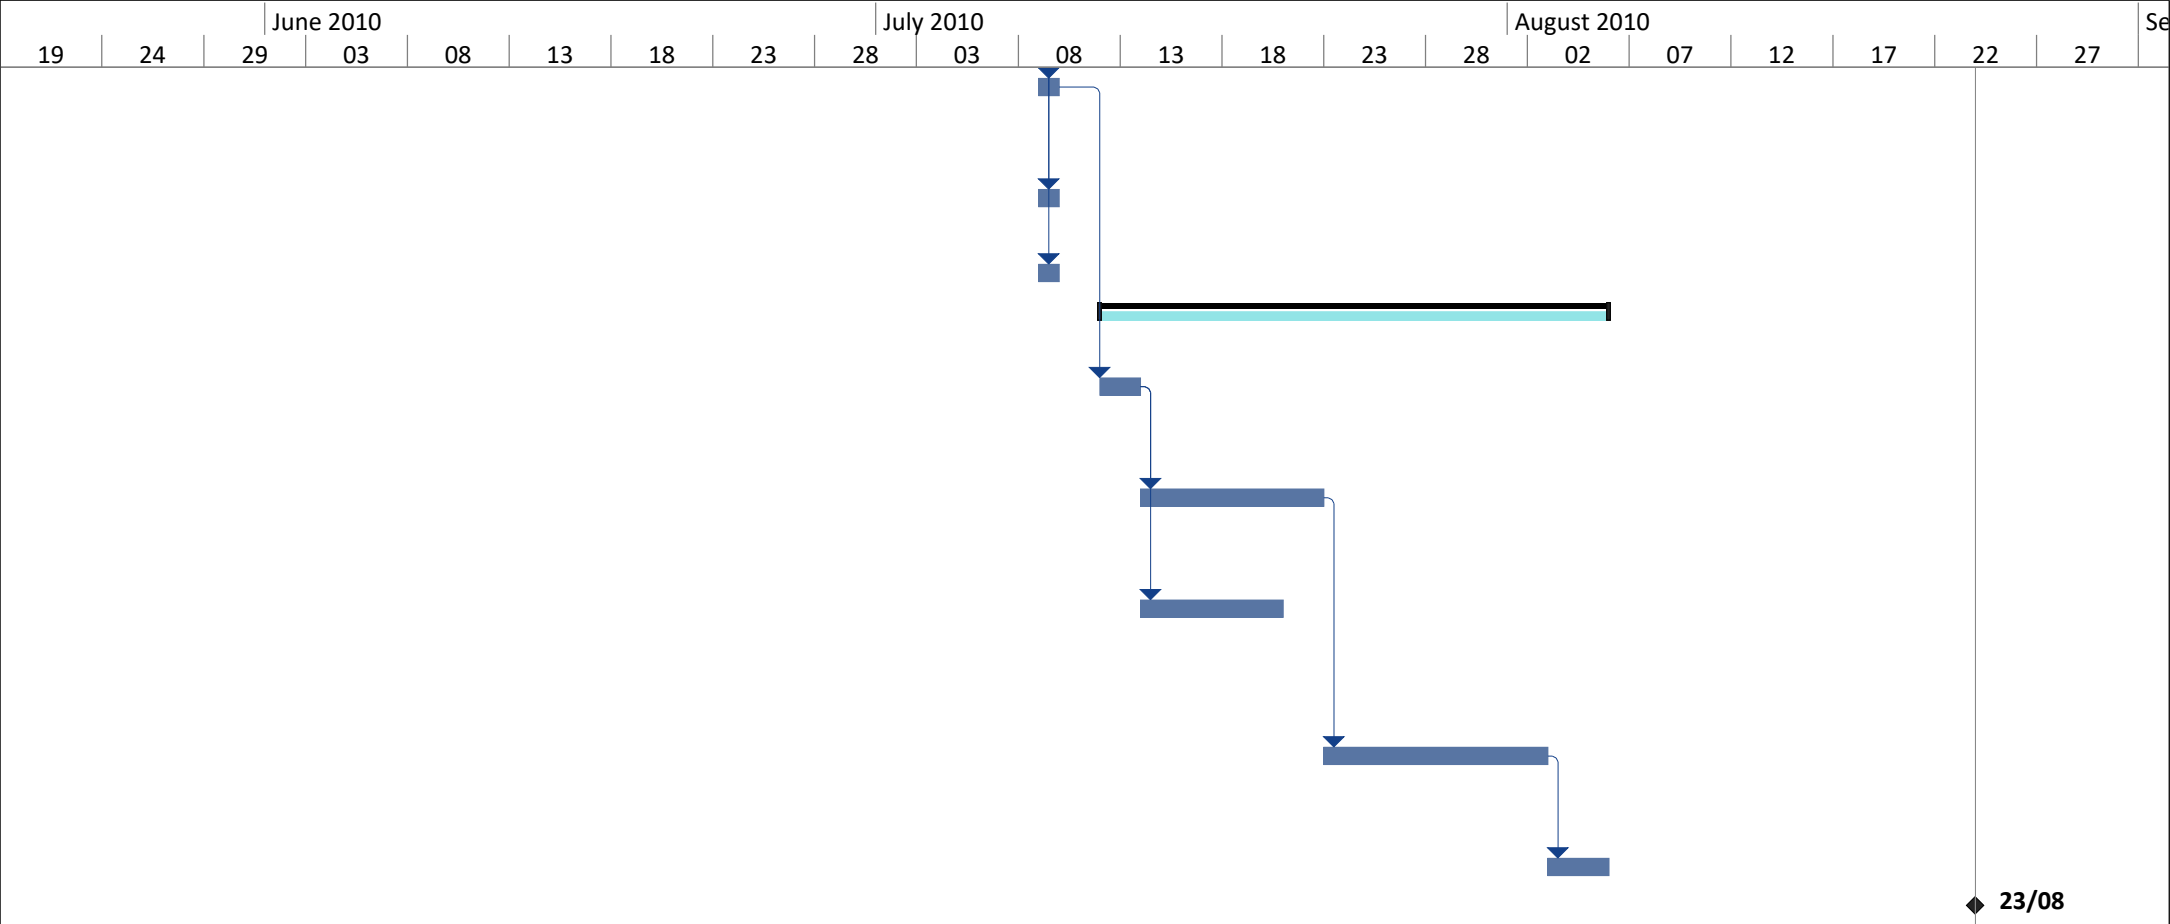

|                                         |                    |  |                       |  |                 |  |
|-----------------------------------------|--------------------|--|-----------------------|--|-----------------|--|
| Project: msproj11<br>Date: Tue 25/11/25 | Task               |  | Inactive Task         |  | Start-only      |  |
|                                         | Split              |  | Inactive Milestone    |  | Finish-only     |  |
|                                         | Milestone          |  | Inactive Summary      |  | Deadline        |  |
|                                         | Summary            |  | Manual Task           |  | Progress        |  |
|                                         | Project Summary    |  | Duration-only         |  | Manual Progress |  |
|                                         | External Tasks     |  | Manual Summary Rollup |  |                 |  |
|                                         | External Milestone |  | Manual Summary        |  |                 |  |
